

NGT MATTER

By Special Messenger / Email

	DELHI POLLUTION CONTROL COMMITTEE DEPARTMENT OF ENVIRONMENT, GOVT. OF NCT OF DELHI 3rd FLOOR, IT PARK BUILDING, SHASTRI PARK, DELHI -110053 visit us at : http://dpcc.delhigovt.nic.in
---	---

F. No. DPCC/WMC-II/MPR/OA 673/2020/792-795

Dated: 19/05/2025

To,

The Secretary,
Ministry of Jal Shakti, Govt. of India,
Shram Shakti Bhawan,
New Delhi- 110001


Subject – Monthly Progress Report of Govt. of NCT of Delhi for the Month of April, 2025, w.r.t Orders Dated 06.12.2019, 29.06.2020, 21.09.2020 & 22.02.2021 in OA No. 673 / 2018 in the matter of News item published in 'The Hindu' Authored by Shri Jacob Khoshy Titled "More river stretches are now critically polluted: CPCB"

Sir,

Please find enclosed herewith Monthly Progress Report of Govt. of NCT of Delhi, on the basis of inputs received from the agencies concerned, in the Format of NMCG for the April, 2025 w.r.t Orders Dated 06.12.2019, 29.06.2020 21.09.2020 & 22.02.2021 in OA No. 673 / 2018 in the matter of News item published in 'The Hindu' Authored by Shri Jacob Khoshy Titled "More river stretches are now critically polluted: CPCB".

1st Monthly Progress Report of Govt. of NCT of Delhi was submitted vide letter dated 14.02.2020 & last Monthly Progress Report for the month of March, 2025 was submitted vide letter dated 21.04.2025.

Yours Sincerely,




(Dr. K.S. Jayachandran)

Spl. Secy (Env) cum
Member Secretary, DPCC

Enclosure: As Above

Copy to:

1. The Member Secretary, Central Pollution Control Board, Parivesh Bhawan, East Arjun Nagar, Delhi-110032.
2. The Staff Officer to Chief Secretary, 5th Floor, Delhi Secretariat, I.P. Estate, Delhi-110002
3. PS to Chairman, DPCC.



(Dr. K.S. Jayachandran)

Spl. Secy (Env) cum
Member Secretary, DPCC

National Mission for Clean Ganga
Format for Submission of Monthly Progress Report in the NGT Matter OA No. 673 of
2018 (in compliance to NGT order dated 24.09.2020)
For the State of NCT of Delhi

Monthly Progress Report of Govt. of NCT of Delhi for the Month of April, 2025

Overall Status of the State:

I. Total Population: Urban Population & Rural Population separately

	Population as per Census in 2011 (in Lakh)	Population in Jan, 2025 (Approx. Estimated) (in Lakh)
Urban Population	163.68899	215
Rural Population	4.19042	
Total	167.87941	215

II. Estimated Sewage Generation (MLD) : 3600 MLD (792 MGD) (80 % of 990 MGD Water Supply)

III. Details of Sewage Treatment Plant:

- Existing No. of Operational STPs of DJB : **37 STPs** (at 21 Locations)
- Installed Treatment Capacity of 37 Operational STPs : **3474 MLD (764 MGD)**
 [Including New 124 MGD Okhla STP & New 7 MGD Sonia Vihar STP] (96.5 % of estimated sewage generation)
- Capacity Utilization of existing STPs : **2783.7 MLD (612.3 MGD)**
 (80.14 % of Treatment Capacity)
- MLD of sewage being treated through Alternate technology : Nil

• Gap in Treatment Capacity • Gap in Treatment • No. of Operational STPs • No. of Complying STPs • No. of Non-complying STPs	: 127.3 MLD (28 MGD) [792 – 764 MGD] (3.5 %) : 816.7 MLD (179.7 MGD) [792 – 612.3 MGD] (22.7 %) : 37 (Refer Annexure-1) : 21 w.r.t. Standards prescribed by DPCC (BOD/TSS: 10/10 mg/l) : 16 (Letters are issued regularly to DJB for taking rectification measures to meet the prescribed standards). Following 21 STPs (Total 531 MGD Capacity) are designed for BOD/ TSS : 10 / 10 mg/l <table border="0"> <tr> <td>1. Pappankalan Phase II (20 MGD)</td><td>2. Nilothi Phase II (20 MGD)</td></tr> <tr> <td>3. Delhi Gate Phase II (15 MGD)</td><td>4. Kapashera (5 MGD)</td></tr> <tr> <td>5. Chilla (9MGD)</td><td>6. Common Wealth Games Village (1 MGD)</td></tr> <tr> <td>7. Coronation Pillar New STP (70 MGD)</td><td>8. Kondli STP Phase-I (10 MGD)</td></tr> <tr> <td>9. Kondli STP Phase-II (25 MGD)</td><td>10. Kondli STP Phase-III (10 MGD)</td></tr> <tr> <td>11. Kondli STP Phase-IV (45 MGD)</td><td>12. Rithala Phase I (40 MGD).</td></tr> <tr> <td>13. New Okhla STP (124 MGD)</td><td>14. Sonia Vihar (7 MGD)</td></tr> <tr> <td>15. Yamuna Vihar Phase –II (15 MGD)</td><td>16. Coronation Pillar Ph- I&II (20 MGD)</td></tr> <tr> <td>17. Coronation Pillar Ph- III (10 MGD)</td><td>18. Narela (15 MGD)</td></tr> <tr> <td>19. Rithala Phase –II (40 MGD)</td><td>20. Rohini (25 MGD)</td></tr> <tr> <td>21. Najafgarh (5 MGD)</td><td></td></tr> </table> Delhi Gate Phase I STP (2.2 MGD) & Sen Nursing Home STP (2.2 MGD) are designed for BOD/ TSS : 10 / 15 mg/l Standards prescribed by DPCC for STPs of DJB in Delhi as per the directions of CPCB (More Stringent than prescribed by MoEF&CC) : (i) pH - 6.5 - 9.0 (ii) TSS ≤ 10 mg/l (iii) BOD ≤ 10 mg/l (iv) COD ≤ 50 mg/l (v) Ammonical Nitrogen ≤ 5mg/l (vi) Total Nitrogen (N-Total) ≤ 10 mg/l (vii) Phosphate (PO₄ - P) ≤ 2 mg/l (viii) Fecal Coliform (FC) (MPN/100ml) < 230	1. Pappankalan Phase II (20 MGD)	2. Nilothi Phase II (20 MGD)	3. Delhi Gate Phase II (15 MGD)	4. Kapashera (5 MGD)	5. Chilla (9MGD)	6. Common Wealth Games Village (1 MGD)	7. Coronation Pillar New STP (70 MGD)	8. Kondli STP Phase-I (10 MGD)	9. Kondli STP Phase-II (25 MGD)	10. Kondli STP Phase-III (10 MGD)	11. Kondli STP Phase-IV (45 MGD)	12. Rithala Phase I (40 MGD).	13. New Okhla STP (124 MGD)	14. Sonia Vihar (7 MGD)	15. Yamuna Vihar Phase –II (15 MGD)	16. Coronation Pillar Ph- I&II (20 MGD)	17. Coronation Pillar Ph- III (10 MGD)	18. Narela (15 MGD)	19. Rithala Phase –II (40 MGD)	20. Rohini (25 MGD)	21. Najafgarh (5 MGD)	
1. Pappankalan Phase II (20 MGD)	2. Nilothi Phase II (20 MGD)																						
3. Delhi Gate Phase II (15 MGD)	4. Kapashera (5 MGD)																						
5. Chilla (9MGD)	6. Common Wealth Games Village (1 MGD)																						
7. Coronation Pillar New STP (70 MGD)	8. Kondli STP Phase-I (10 MGD)																						
9. Kondli STP Phase-II (25 MGD)	10. Kondli STP Phase-III (10 MGD)																						
11. Kondli STP Phase-IV (45 MGD)	12. Rithala Phase I (40 MGD).																						
13. New Okhla STP (124 MGD)	14. Sonia Vihar (7 MGD)																						
15. Yamuna Vihar Phase –II (15 MGD)	16. Coronation Pillar Ph- I&II (20 MGD)																						
17. Coronation Pillar Ph- III (10 MGD)	18. Narela (15 MGD)																						
19. Rithala Phase –II (40 MGD)	20. Rohini (25 MGD)																						
21. Najafgarh (5 MGD)																							

- **Sewage Treatment Capacity Augmentation Plan of Delhi to meet the Gap and Accommodate future Increase in Sewage Generation:**

Govt. of NCT of Delhi is primarily working on following 4 Sectors for augmenting the sewage treatment capacity in Delhi and details are given in following Table:

- Rehabilitation of existing 3 STPs at Kondli Ph-II , Rithala Ph-I (Both are under Test & Trial Run) and Yamuna Vihar Ph –II (Rehabilitation near completion)
- Upgradation and increasing capacity of remaining 18 existing STPs (Upgradation completed in case of 7 STPs)
- Construction of 3 New STPs at Okhla (Completed and under Trial Run & Commissioning in progress), Sonia Vihar (Completed under Trial Run) and Delhi Gate (Land Allotted).
- Construction of 40 DSTPs [26 DSTPs at various locations of Delhi and 14 DSTPs in Najafgarh Drainage Zone]

Rehabilitations of existing STPs and construction of New STPs/DSTPs

[Treatment Capacity of 764 MGD of 37 STPs]

S.No	Name of STP	Capacity Addition (in MGD)	Timelines
Sewage Treatment Plants			
1	Okhla (New STP) of 124 MGD Capacity (Under Construction) Physical Progress : 100 %	30*	Completed. Plant is under trial run. (already included in 764 MGD capacity)
2	Sonia Vihar (New STP) of 7 MGD Capacity (Under Construction) Physical Progress : 100 %	07*	Completed. Plant is under trial run. (already included in 764 MGD capacity)
3	Delhi Gate (New STP) of 10 MGD Capacity DDA/ MoHUA has allotted the land on 03.04.2025.	10	June, 2027
4	Kondli Phase- II of 25 MGD Capacity Physical Progress: : 98.2 % Progress in April, 2025 : 0 % Liquid line started on 24.06.2023.		Completed. Plant is under trial run. (already included in 764 MGD capacity)
5	Rithala Phase – I of 40 MGD Capacity	-	Completed. Plant is under trial run. (already included in 764 MGD capacity)
6.	Yamuna Vihar Ph-II (From 10 MGD to 15 MGD, Under Rehabilitation & Up-gradation, Presently in operation with 15 MGD Capacity) Physical Progress : 99% Progress in April, 2025 : 1 %	05*	Revised Time Line to be informed by DJB (Earlier Timeline Sept. 2023) (already included in 764 MGD capacity)
	Total Addition in Capacity of STPs	10 MGD	

Status of 40 New Proposed Decentralised Sewage Treatment Plants (DSTPs) [92MGD]		
A. 26 DSTPs of total Capacity of 60 MGD		
24 DSTPs (Land already allotted)	38 DSTPs (87 MGD) – By June, 2027 02 DSTPs (5 MGD) – Land yet to be allotted by DDA / Revenue Department	
Two DSTPs [Land is yet to be allotted for Proposed DSTPS at Nayabans & Maidan Garhi (Rajpur Khurd)]		
B. 14 DSTPs in Najafgarh Drainage Zone of total Capacity of 32 MGD		
14 DSTPs (Land already allotted)		
C. Up-gradation / Augmentation of Remaining 10 Existing STPs of total Capacity of 98.5 MGD	98.5	June, 2027
Grand Total Capacity by June, 2027	764 + 200.5 =964.5MGD#	

Total Capacity of STPs by Sept., 2025 - 814 MGD [764 MGD + 50 MGD]

Total Capacity of STPs by June, 2027 - 964.5 MGD [764 MGD + 200.5 MGD]

Will be sufficient to treat the sewage of 924.8 MGD (80% of 1156 MGD Water Supply) in future.

All the STPs (existing as well as new) with total capacity of 964.5 MGD are targeted to achieve standards prescribed by DPCC i.e BOD / TSS: 10/10 mg/l by June, 2027.

Details of Each Existing STP of Delhi Jal Board in Delhi

S. No.	Location	Existing STP Capacity	Capacity Being Utilized	Operational Status of STP	Compliance Status of STP
	Details of Each Existing STP of Delhi Jal Board in Delhi and Compliance status for the month of April, 2025 is at <u>Annexure-1</u>				

Details of Upgradation / Augmentation of Existing 18 STPs of DJB are at **Annexure-2**

Details of Proposed STPs of Delhi Jal Board in Delhi

S. No.	Location	Capacity of STPs proposed (in MGD)	Status of Project (at DPR Stage/ Under Tendering/ Work to be Awarded)	Likely Date of Completion
1.	42 Decentralized STPs at various locations in Delhi	281.50	- Requirement of land reassessed - No. of DSTPs reduced from 42 to 26 - Land allotted at 24 locations - For balance 2 DSTPs proposed at Nayabans & Maidan Garhi (Rajpur Khurd) matter is being pursued with land owning agencies (DDA / Revenue Deptt.). - At one location of Naya Bans, part of land is allotted and for balance matter is being pursued with land owning agencies. Tenders are being invited for DSTPs /STPs where land has been allotted. At Jindpur, funds are approved in AMRUT 2.0. For rest of places, Estimates has been cleared by EFC. Case is expected very soon before the Cabinet.	Out of 40 DSTPs, Land has been allotted in case of 38 DSTPs. For 32 DSTPs tenders have been received / invited/ being invited. Out of balance 8, estimate for 6 DSTPs are under approval/ preparation. As per the latest guidelines, AA & ES for these estimates are to be approved by UD

2.	14 (9+5) STPs in Najafgarh Drainage Zone	145	• The work of 14 DSTP has been rescinded. The scheme under 14 DSTP has been reframed to accommodate the maximum nos. of unauthorized colonies in the 14 parcels of land already in possession of DJB. • The status of construction of DSTPs and laying of sewer line is as under : • The work of laying of 3 GOC i.e. Khera Dabar , Kair GOC & Goyla Vihar has been completed. The work of laying of Sewer lines in 08 GOCs of Jafarpur, Galibpur Sarangpur, Kazipur, Shikarpur, Kanganheri, Mitraon and Dichaon is in progress. • Tender for laying of Sewer lines in 1 GOC Hasanpur has been received and is under process of award. This work is under Amrut 2.0 funding. • Land for construction of DSTP for Tajpur Khurd & Tikri kalan GOC have been taken over DJB on 21.06.2024 and 01.07.2024. Estimates for both GOCs has been cleared by EFC. Case is expected very soon before the Cabinet.	Deptt. / EFC /GoM as per the cost. Land for balance 2 DSTP is yet to be allocated by DDA/ Revenue deptt. and expected to be completed within 18 months after award of work.
----	--	-----	--	---

Status of Interceptor Sewer Project (ISP) of Delhi Jal Board

Total flow to be trapped	Provision of trapping made during the month of March, 2025	Cumulative Status as in April, 2025 Provision of trapping made	Time line for completion of work	Remarks
1100.86 MLD (242 MGD)	-	1082 MLD (238 MGD)	Completed	YMC has got an independent assessment done through a team consisting of Sh. R.S Tyagi former Member (Dr) DJB and Prof Singh, Head of Department of Environmental Engineer, Delhi Technical University. Said team has confirmed that sewage trapping part of ISP has indeed been completed. However, treatment of 242 MGD of sewage as planned will take place after construction / rehabilitation of Rithala & Kondli STP.

Status of Sewerage Network in Unauthorized Colonies (As provided by DJB)

Sl. No	Status	Commutative Status (As on 30.04.2025) (No.)
1	No. of Unauthorized Colonies where Sewer line laid	1226
2	No. of Unauthorized Colonies where sewer line work in progress	154
3	No. of Unauthorized Colonies where work is in Estimate /Tender / Award stage.	270
4	No. of Unauthorized Colonies where NOC is awaited from (Forest/ASI/ UD Deptt.)	99
5	No. of Unauthorized Colonies where sewer line will be laid after handing over possession of land for 2 DSTP	33
	Total	1782*

*17 Unauthorized Colonies are not feasible/ cancelled by UD Deptt, Not Traceable / not existing

Sewage and Faecal Sludge Management (Septage Management)

Delhi Water Board Septage Management Regulation 2018” were notified by the Urban Development Department, GNCTD on **12.11.2018 (published in Gazette on 21.11.2018)** and necessary action is to be taken by Delhi Jal Board, District Magistrates and Local Bodies / Municipal Corporations as per the provisions of the said Notification.

Urban Development Department, GNCTD has issued “Delhi Water Board Septage Management (Amendment) Regulation, 2024” on 13.03.2024 including following amendments in the existing Regulations :

1. (a) Penalty for deposit of septage by unauthorized (unlicensed) entities shall be Rs. 50,000/- plus confiscation of vehicle.
 - (b) Penalty for disposal of Septage at places other than the designated places by authorized licensee shall be Rs. 50,000/- per violation.
 - (c) Penalty on a person who uses the services of unlicensed vendors/vehicles for discharging the septage shall be Rs. 10,000/- per violation.
2. An officer not lower than the rank of Naib Tehsildar in DM offices, JE in DJB/I&FC, Sub Inspector in Delhi Police and Sanitary Inspector in CD shall be competent to impose penalty.

Installation of GPS System - Each Vehicle used for transportation of septage shall be fitted with GPS device and access rights of the movement data shall be given to the Delhi Jal Board for tracking of such vehicles.

Brief of septage (Septic Tank Effluent) collected & treated in April, 2025 is given in following Table:

No of Vehicles Authorised by DJB	No. of Functional SPSs for collection of septage from vendors	Septage collected & Treated in April, 2025	Cumulative Septage Treated by DJB (As on 27.04.2025)
164	86	2.42 Crore Litres	241.7 Crore Litres

On an average about 8.96 Lakh liters septage per day was collected and treated at STPs of DJB in April, 2025.

Tapping of Drains:

There are 22 drains which are out falling into river Yamuna in the Delhi and brief is as follows :

- 09 Drains have been tapped
- 02 Drains (Delhi Gate Drain & Sen Nursing Home Drain) are Partially Tapped.
- 02 Drains (Najafgarh & Shahdara) are large drains and technically not feasible to tap whole drain however these drains are included in the Interceptor Sewer Project where substantial flow of sub-drains under their command areas has been / will be tapped and treated after tapping of sub drains.
- Out of remaining 09 Drains, DJB has informed regarding tapping of Sonia Vihar Drain however flow was observed by DPCC Lab & sample was taken on 06.12.2024, 10.01.2025, 10.02.2025, 05.03.2025, 07.04.2025 & . Flow is yet to be tapped / diverted to Sewer / STPs for treatment in case of remaining 08 drains.
- Information about 22 Drains out falling into River Yamuna in Delhi, their Water Quality in April, 2025 and proposed action for tapping of flow in 9 drains is at **Annexure - 3.**

IV. Details of Industrial Pollution | Industries/Units in 28 Approved Industrial Areas (Planned Industrial Areas) in Delhi | (As per the Consent Records of DPCC) (As on 30.11.2024):

- No. of Industries / Units in 28 Approved Industrial Areas : 29823
- No. of Industries / Units in 17 Approved Industrial Areas (out of 28 Approved Industrial Areas) connected with 13 CETPs : 26404
- No. of Industries / Units in 11 Approved Industrial Areas (out of 28 Approved Industrial Areas) not having CETPs (Having Individual ETPs). : 3419
- No. of Water Polluting Industries / Units in 28 Approved Indl. Areas : 1411
- No. of Water Polluting Industries/ Units in 17 Approved Indl. Areas (out of 28 Approved Indl. Areas) connected with 13 CETPs : 1111
- No. of Water Polluting Industries/ Units in 11 Approved Indl. Areas (out of 28 Approved Indl. Areas) not having CETPs (Having Individual ETPs) : 300
- Quantity of Effluent generated from the Industries / Units in 28 Approved Indl. Areas (Excluding White Category Industries/Units, Shops & Other Establishments not requiring Consent from DPCC) : 32.79 MLD
- Quantity of Effluent generated from the Industries / Units in 17 Approved Industrial Areas (out of 28 Approved Indl. Areas) Not having CETPs (Excluding White Category Industries/Units, Shops & Other Establishments not requiring Consent from DPCC) : 25.89 MLD
- Quantity of Effluent generated from the Industries / Units in 11 Approved Industrial Areas (out of 28 Approved Indl. Areas) Not having CETPs (Excluding White Category Industries/Units, Shops & Other Establishments not requiring Consent from DPCC) : 6.90 MLD
- Quantity of Hazardous Waste generated from the Industries in TPD (including CETPs) : 11.67 TPD
- Number and total capacity of ETPs (details of Existing/ Under Construction / Proposed) : 1411 ETPs
- Compliance Status of the ETPs : -
- Number and Total Capacity of CETPs (Details of Existing/ Under Construction / Proposed) : Existing CETPs-13(List at **Annexure-4**)
Capacity – 212.3 MLD
(Utilization –73.419 MLD (34.58 %)
Under Construction/Proposed – Nil

Redevelopment Areas

Besides 28 Approved Industrial Areas, there are 26 Areas Notified for Re-development (non-conforming clusters of industries for redevelopment) by the Industries Department, Govt. of NCT of Delhi. Details regarding no. of industries/units in these 26 redevelopment areas are not available. Most of the industries/ units in these areas are dry and there is not much water polluting industries / units in these Redevelopment Areas. List of 26 Redevelopment Areas Notified for Re-development has already been provided through Monthly Progress Report of August, 2023.

These Redevelopment Areas are lacking infrastructural facilities which are to be developed as per the norms for redevelopment of clusters of Industrial Concentration in Non-Conforming Areas as given in point no. 7.6.2.1. of MPD- 2021. The redevelopment scheme of these unplanned Industrial Areas will have to be prepared by the concerned local body / land owning agency in consultation with the Society (to be formed by the land owners). Accordingly, the redevelopment of these 26 industrial areas is to be done by concerned local body/landowning agency.

Status of Compliance and Operation of the CETPs

Town	No. of Industries/ Units (in 28 Approved Industrial Areas)	Industrial Discharge	Status of ETPs	Status of CETPs (Existing, Under Construction & Proposed)
Delhi	29823	32.79 MLD	-	Existing – 13 CETPs List along with Compliance Status of April, 2025 is at <u>Annexure-4</u> Under Construction / Proposed - Nil Complying - 09 Not Complying – 04 (CETP Wazirpur, CETP Narela, CETP Okhla & CETP GTK) Brief of Action Taken by DPCC against CETPs in the past is as follows : • Environmental Compensation (Total EC Amount of Rupees 19.10 Crores) has been imposed by DPCC on the 11 CETP Societies and 2 Operators of CETPs at Narela & Bawana from time to time for violations / not meeting the prescribed standards in the past. • Letter issued to concerned District Magistrates for recovery of the said amount of Environmental Compensation on 27.10.2021, 12.01.2022 in Year 2023 also. • CETP Societies of Okhla, SMA, Mayapuri, Mangolpuri, GTK Road, Naraina, Jhilmil & Lawrence Road (Total 8 Cases) filed Writ Petition in the High Court of Delhi against the Directions issued by DPCC regarding imposition of Environmental Compensation and cases are at various stages. • Letters are issued regularly to the concerned CETP Societies based on the Effluent Analysis Reports of DPCC Lab for taking necessary action to ensure that CETPs meet the prescribed standards.

Common Effluent Treatment Plants (CETPs)

All the existing 13 CETPs are being monitored by DPCC Laboratory on monthly basis and Analysis Reports are placed on the website of DPCC and also conveyed to the CETP Societies / Operator of CETPs for rectification of the deficiencies, if any, to meet the prescribed standards. Sufficient treatment capacity (212.3 MLD) is available with existing 13 CETPs for management of industrial effluent generated from 17 approved industrial areas. The units which are operational in Non-CETP Industrial Areas have individual waste water treatment facilities (ETP etc). All the 13 CETPs are having Online Continuous Effluent Monitoring System (OCEMS) for measuring the pH, TSS, BOD & COD at the outlet of the CETPs. OCEMS are connected to the servers of DPCC and CPCB.

DSI IDC had engaged CSIR-NEERI vide letter dated 05.11.2019 for providing consultancy w.r.t various issues related to CETPs including up gradation of CETPs.

NEERI carried out Overall Performance Evaluation of all the 13 CETPs in Delhi and Draft Integrated Report titled "Status, Gap Analysis and Suggestions for Improvement and Upgradation in existing 13 CETPs of Delhi" submitted to DSI IDC on 16.03.2022.

In view of the Order dated 27.01.2023 of Chief Secretary, GNCTD issued w.r.t NGT Order dated 09.01.2023 in OA No. 21 / 2023, Out of 13 CETPs, 02 CETPs at Narela and Bawana were to be upgraded by DSI IDC and Rest 11 by DJB after taking over of these 11 CETPs from the concerned CETP Societies.

Govt. of NCT of Delhi vide Notification dated 01.01.2024 had given powers in respect of 11 CETPs presently being operated and maintained by CETPs Societies to DJB however the said Notification regarding taking over of these CETPs by DJB from the concerned CETPs Societies has been quashed by Hon'ble High Court of Delhi and Industries Department of Govt. of NCT of Delhi is taking further necessary action in the matter.

As informed by DSIIDC, work of Upgradation of CETPs at Narela & Bawana has been completed.

V. Solid Waste Management:

- Total Number of Urban Local Bodies (ULBs) : 3 [MCD, NDMC & DCB]
and their Population Total Population – About 2.15 Crores
 - Current Municipal Solid Waste Generation : **11342 TPD**
- (Status of Solid Waste Management including Legacy Waste in Delhi is given at **Annexure-5**)

S. No.	Particulars	Information
1.	Number, Installed Capacity and Utilization of Existing MSW Processing Facilities in TPD (Bifurcated by type of processing e.g. Waste to Energy (Tonnage and Power Output), Compost Plants (Windrow, Vermi, Decentralized, Pit Composting), Biomethanation, MRF etc.	• Total Capacity of Existing MSW Processing Facilities (Including MRFs) - 8173 TPD (72 %) • Total MSW Processing (Fresh MSW + MRFs) - 6670.6 TPD (58.84%) • Disposal through Compost Pits (257 No) - 558 TPD • Recycling through 176 MRFs (Capacity) - 322 TPD • Gap in MSW Processing Capacity - 3169 TPD (28 %) • Gap in MSW Processing - 4671.4 TPD (41.2 %) • Capacity of 4 Existing WTE Plants - 6550 TPD • (Power generation capacity – 84 MW) • One Operational Centralised Compost Plant - 700 TPD [200 TPD at Okhla Closed due to up-gradation into Bio-CNG plant of 300 TPD] • 20 Decentralized Composter Plants of 1 TPD each - 20 TPD
2.	Action Plan to bridge gap between Installed Capacity and Current Utilization of Processing Facilities (if Gap > 20%)	Not Applicable since installed capacity of Existing MSW Processing Facilities in Delhi is being utilized (More than 80 % Capacity utilization)
3.	No. and capacity of C&D Waste Processing Plants in TPD (Existing, Proposed and under construction)	• Existing operational C&D Waste Processing Facilities Capacity - 5150 TPD • Proposed New C&D Waste Processing Facilities Capacity - 1000 TPD Existing operational C&D Waste Processing Facilities are located at (i) Jahangirpuri (Burari) (2000 TPD) (ii) Rani Khera (1000TPD) (iii) Shastri Park (1000 TPD) (iv) Bakkarwala (1000 TPD) (v) Rani Khera (Mundka of DMRC) (150 TPD) Proposed C&D Waste Processing Facility (One No): One C&D Processing Facility of 1000 TPD capacity in 7 acres of reclaimed land at Okhla Dumpsite for 2 zones i.e. Central and South is proposed. The financial bid opened on 30.10.2024 and Rate & Agency has been approved by the Competent Authority and Letter of Intent has been given to the Agency. The Likely date of commissioning will be December 2026.

4.	Total No. of Wards, No. of Wards having Door to Door Collection Service, No. of Wards practicing segregation at source	No. of Wards - 272 [MCD-250, DCB-08 & NDMC-14 Circles] Door to Door collection in all wards and circles of MCD, NDMC & DCB. Segregation of Waste : • NDMC- > 92 % (in all 14 Circles) • DCB - 90% in Civil Pockets & 70 % in Army Pockets (100 % segregation at source by June, 2025) • MCD - 60 % (Average) Timelines for segregation : 75% by Aug., 2025, 85 % by, Feb., 2026 90 % by Aug., 2026 100 % January, 2027 • No. of Zero Waste Colonies / Institutes – 633	
5.	Details of MSW Treatment Facilities proposed and under construction (No., Capacity and technology)	Proposed Waste Processing & Disposal Facilities in Delhi is given at <u>Annexure -5</u>	
6.	No. and Area (in Acres) of uncontrolled garbage dumpsites and Sanitary Landfills.	Name of Dumpsite	Dumpsite Area in Acres (As per Drone Survey in June, 2022)
		Ghazipur Dump Site	75.08
		Bhalaswa Dump Site	78.47
		Okhla Dump Site	62.74
7.	No. and Area (in Acres) of Legacy Waste within 1 km buffer of both side of the rivers	Nil	
8.	No. of Drains falling into rivers and no. of drains having floating racks/screens installed to prevent solid waste from falling into the rivers:	22 Drains out falling into river Yamuna. I&FC Department has provided Floating Rafters in its 2 major Drains (Najafgarh & Shahdara Outfall Drains) to prevent solid waste falling into the river.	

Status of ULB wise Management of Solid Waste .

Please Refer **Annexure – 5** (Existing & Proposed Municipal Solid Waste Processing Facilities in Delhi)

VI. Bio-medical Waste Management:

- Total Bio-medical Waste Generation : **31.201 TPD**
- No. of Hospitals and Health Care Facilities : **10974**
- No. of Beds with HCEs : **61581**
- Status of Treatment Facility/ CBMWTF : Treatment & Disposal through existing 2 CBMWTFs
There are following 2 CBMWTFs having Capacity of 62.8 TPD for collection and Treatment of the Bio-medical waste generated from the Health Care Establishments in Delhi:

1. M/s Biotic Waste Solutions Pvt. Ltd., 46-47, SSI Industrial Area, G.T. Karnal Road, Delhi -33
2. M/s SMS Water Grace BMW Pvt. Ltd., Nilothi Sewage Treatment Plant Complex of DJB, Nilothi, Delhi -41.

Both the CBMWTFs are having Incinerators, Autoclaves & Shredders for the treatment of Bio Medical Waste collected from the Health Care Establishments in Delhi and have installed Air Pollution Control System and Online Monitoring System. Bio-medical Waste including Covid – 19 waste is being dealt as per the provisions of the Bio Medical Waste Management Rules, 2016 and Guidelines issued by CPCB from time to time.

VII. Hazardous Waste Management:

- Total Hazardous Waste Generation : 4260.587 MT/year (11.67 TPD)
- No. of Industries generating Hazardous Waste : 2714
- Treatment Capacity of all TSDF
(There is only one TSDF in Delhi at Bawana) : 178 TPD (Secured Landfill)
54.79 TPD (Landfill after Treatment /
Stabilisation) 12 (Incineration)

Average Quantity of Hazardous Waste reaching TSDF : 13.95 TPD in April, 2025.

● TSDF for Hazardous Waste at Bawana :

Common Hazardous Waste, Treatment, Storage & Disposal Facility (TSDF) has been developed at Bawana in Delhi. Consent to operate under the Air & Water Acts and Authorisation under the Hazardous and Other Wastes (Management and Transboundary Movement) Rules, 2016 have been issued by DPCC to the Project Proponent on 04.03.2022 for Secured Land Fill (SLF), Incinerator and Associated Activities. TSDF is in operation.

VIII. Plastic Waste Management:

- Total Plastic Waste generation : 1117 TPD (About 9.8 % of Total MSW)
- Processing of Plastic Waste : 858 TPD (76.8 %)
- Gap in Processing : 259 TPD (23.2 %)
- Registration under the Plastic Waste Management Rules, 2016 (as amended) issued to 2199 units as briefed below:
 - Producers : 320
 - Importers : 1445
 - Brand Owner : 15
 - Plastic Waste Processor : 419

IX. Details of Alternate Treatment Technology being adopted by the State/UT:

In-situ Bioremediation / Phytoremediation of Sewage in Drains:

- Integrated Drain Management Cell (IDMC) headed by Chief Secy, GNCTD has been constituted vide order dated 17.03.2020 issued by Urban Development Department, Govt. of NCT of Delhi pursuant to the order dated 05.03.2020 of Hon'ble National Green Tribunal in OA No. 06/ 2012 in the matter of Manoj Mishra Vs. Union of India & Ors, for remediation and management of all drains of Delhi.
- IDMC is having members from all the Drain Owning Agencies (DOAs).
- Meetings of IDMC are held and 20 Meetings have been held so far. Last meeting (20th) of IDMC was held on 17.03.2025.
- DOAs have submitted / are submitting their Action Plan with time line subject to availability of fund.
- IDMC is also taking action w.r.t directions of the Hon'ble High Court of Delhi in the order dated 08.04.2024 & subsequent orders passed in WP(C) No. 9617/2022 in the matter Court on its own Motion Vs Govt. of NCT of Delhi & Ors regarding Flooding in Delhi.

X. Identification of Polluting Sources including Drains contributing to river pollution and action as per NGT order on in-situ treatment:

Refer Information provided at IX regarding In-situ Bioremediation / Phytoremediation of Sewage in Drains.

Prevention of Dumping of Solid Waste in Drains:

Directions issued by Chief Secretary vide order dated 09.01.2019 and Urban Development Department, GNCTD vide order dated 15.01.2019 for prevention of the dumping of solid waste in the drains are to be complied by all the Drain Owning Agencies in Delhi. The matter is being coordinated by the Urban Development Department, GNCTD.

XI. Details of Nodal Officer appointed by Chief Secretary in the State / UT:

- Chief Secretary, GNCTD is taking meetings regularly with the concerned departments to review the progress w.r.t. various projects and matters related to control of pollution in river Yamuna in Delhi including below mentioned NGT cases.
- Vide order dated 09.01.2023 in OA. No. 21/2023 in the matter of Ashwani Yadav Vs. Govt. of NCT of Delhi (Now being dealt in O.A. No. 06 of 2012 in the matter of “Nizamuddin West Association Vs. Union of India and Ors”), Hon’ble NGT has constituted a High Level Committee (HLC) of concerned authorities in Delhi with the Chief Secretary, Delhi, as Convener; and consisting of Secretaries / HODs of various Ministries/ Departments.
- High Level Committee has prepared Department wise detailed Action Plan for Rejuvenation of river Yamuna including Nodal Officer for each project after its first meeting on 20.01.2023 and submitted to Hon’ble NGT on 31.01.2023.

XII. Details of Meetings carried under the Chairmanship of Chief Secretary in the State / UT:

The matter related to control of pollution in river Yamuna is being monitored by Chief Secretary through various meetings e.g. meetings of Integrated Drain Management Cell (IDMC), Meetings on the Interceptor Sewer Project (ISP) and Meetings related to above mentioned NGT cases related to control of pollution and rejuvenation of river Yamuna in Delhi including above mentioned order dated 09.01.2023 in OA. No. 21/2023 in the matter of Ashwani Yadav Vs. Govt. of NCT of Delhi (Now being dealt in O.A. No. 06 of 2012 in the matter of “Nizamuddin West Association Vs. Union of India and Ors”).

Meetings of High Level Committee were held on 20.01.2023, 14.02.2023, 14.03.2023, 21.04.2023, 09.06.2023, 10.08.2023, 10.10.2023, 10.01.2024, 20.02.2024 & 23.07.2024 w.r.t above mentioned NGT Case and Department wise detailed Action Plan for Rejuvenation of river Yamuna has been submitted to Hon’ble NGT on 31.01.2023.

Status Reports were also filed in the aforementioned matter before the Hon’ble National Green Tribunal on 31.01.2023, 05.07.2023, 16.10.2023, 21.12.2023 & 12.02.2024.

XIII. Latest Water Quality of polluted river, its tributaries, drains with flow details and ground water quality in the catchment of polluted river :

Water Quality of River Yamuna at 8 Locations for the samples collected by DPCC Water Laboratory in the Month of April, 2025 is at **Annexure- 6.**

Water Quality of major Drains for the samples collected by DPCC Water Laboratory in the Month of April, 2025 is at **Annexure-7.**

Ground Water Quality nearby Ghazipur Dumpsite, Bhalswa Dumpsite, Okhla Dumpsite & Bawana Engineered Landfill was monitored by DPCC Laboratory on 1st / 2nd May, 2024 and Copy of the Analysis Reports have already been submitted vide Monthly progress reports of July to October 2024.

XIV. Ground Water Regulation:

Ground water extraction and management in NCT of Delhi is regulated as per the provisions of the Notification Dated 12.07.2010 issued by Environment Department, Govt. of NCT of Delhi.

The issue of illegal extraction of ground water is being overseen by Hon'ble NGT in OA No 25/2019 (Abdul Farukh Vs GNCTD and Ors). The said matter deals with closure of 19661 illegal bore wells as per the list submitted by DJB to Hon'ble NGT. As per the decision taken by the Chief Secretary, GNCTD, Revenue Department is sealing the illegal bore wells based on the lists provided by DJB. DPCC has already imposed Environmental Compensation (EC) based on the formula devised by CPCB for illegal extraction of ground water for different purposes.

Out of list of 19661 illegal Borewells provided by DJB, 11364 illegal Borewells have been sealed by Revenue Deptt. Environmental Compensation of Rs. 70.662 Crore has been imposed by DPCC on 18520 Units. Environmental Compensation received by DPCC is Rs. 73.10 Lakh till 15.02.2025.

XV. Good Irrigation Practices being adopted by the State:

Not applicable in case of NCT of Delhi since there is very less Agricultural Land available however Farmers are being made aware of the following good irrigation practices for water conservation by Development Department, Govt. of NCT of Delhi :-

1. Farmers are being advised to adopt inter-cropping and multiple-cropping to get maximum returns per unit of area and per unit of time with optimum use of water.
2. Farmers are being advised to grow crop which requires less water.
3. Farmers are being advised to adopt Sprinkler and drip irrigation system to irrigate their crops for conservation of water.
4. Farmers are being advised to use water, as per crop-wise prevailing package of practices to conserve water.
5. Farmers are being advised to conserve rain water, by adopting deep ploughing and bunding etc. of their fields for conservation of water.

XVI. Rain Water Harvesting:

Progress of Rain Water Harvesting System installed / monitored by DJB (As on 29.04.2025)

S. No	Departments	Total	Installed	Target to be installed upto 31.07.2025	Not Feasible	Remarks
1.	DJB Installations	594	594	0	0	
2.	By DJB for other Departments	89	89	0	0	
3.	Monitored by DJB for other Government Departments	3598	2545	671	382	The Status Report has been submitted as per data provided by the other departments of GNCTD.
4.	Schools	4892	4371	183	338	
	Total	9173	7599	854	720	

They need to be kept in operational state by the agency concerned.

XVII. Demarcation of Floodplain and Removal of Illegal Encroachments:

(i). Demarcation of 1 in 25 years Flood Plains & Fixing up of Bollards and Fencing :

The demarcation of 1 in 25 years flood plain of River Yamuna pertains from Wazirabad to Jaitpur on both banks. 100% work for demarcation of flood plains completed. 591 Bollards (marked with GPS Coordinates), 375 Flag Posts & 27 sign boards for the entire stretch from Wazirabad barrage to Jaitpur have been installed.

(ii). Engagement of Private Security to stop illegal Dumping:

369 Security Guards have been deployed by DDA round the clock in three shifts at vulnerable points, with 3 patrolling vehicles in the Yamuna Flood Plain area from Wazirabad Barrage to

Okhla Barrage to check illegal dumping of melba and to prevent encroachment. GPS monitoring of security guards & patrolling vehicles is being done.

(iii). Installation of Electronic Surveillance System:

90 No. CCTV cameras have been installed at 27 locations from Wazirabad Barrage to Okhla Barrage to check the illegal dumping of Malba in the Yamuna Flood Plain area.

(iv). Demolition Program & Removal of Encroachment from the Flood Plain:

DDA has been carrying out demolitions to reclaim its land from encroachers. About 1536 acres of land has been reclaimed since 2 years 3 months and more than 10,500 jhuggies / labour huts / semi-pucca structure, 25 religious structures, 7 dairy, 3 cricket grounds, 200 cattle shed, 20 nurseries, 40 Bore well grounds have been demolished.

Details of removal of encroachment by DDA are given at **Annexure- 8.**

(v). Removal of C&D Waste :

80,713 Metric tons of C&D waste & **1160** metric tonnes of garbage lying in floodplain has been lifted to IL&FS site or utilized for development of Yamuna Project by DDA. Details of Challans issued by DDA as on 30.04.2025 are given at **Annexure- 9.**

(vi). Restoration and Rejuvenation of the Floodplains of River Yamuna

DDA is going ahead with the Restoration and rejuvenation of floodplains of River Yamuna. The complete stretch of Zone-‘O’ falling under the jurisdiction of DDA has been subdivided into 10 projects including the development of Bio-diversity Park near Kalindi Kunj Colony. Brief status of 10 projects taken up / to be taken up by DDA for development of Yamuna River Front (Restoration and Rejuvenation of River Yamuna Flood Plains Status as on 30.04.2025) is at **Annexure –10.**

XVIII. Maintaining Minimum e-flow of River:

Minimum Environmental Flow for the dilution of the polluted water in river Yamuna in Delhi is required to meet the desired water quality levels in river Yamuna for bathing purpose i.e. BOD < 3 mg/l & DO > 5 mg/l. To assess the minimum required environmental flow of river Yamuna for stretch between Hathini Kund to Okhla, a comprehensive study was assigned by NMCG to National Institute of Hydrology (NIH), Roorkee on 24.12.2018.

Final Draft Report has been submitted by NIH to NMCG. E-flow of 23 cumecs in the lean season has been recommended in the NIH study. Ministry of Jal Shakti (MoJS) is to take necessary action for maintaining the E-flow as recommended in the said Report of NIH. MoJS / NMCG has observed that the water sharing agreement of 1994 among the riparian states of Uttarakhand, HP, UP, Haryana, Rajasthan and NCT Delhi is due for revision only in 2025 unless any of the states so demand implying that no revision of water sharing will be possible to achieve the E-flow in river Yamuna.

XIX. Plantation activities along the river (Status upto Dec., 2024) :

(i) Details of Old Plantation at Garhi Mandu and Sonia Vihar:

- Total **384.60 ha** of land has been handed over by DDA to Forest Department, Delhi in phases during the period w.e.f. 1975 to 2022 for plantation purpose.
- In **384.60 ha** of land **2,41,184** saplings have been planted by Forest Department, Delhi.

(ii) Details of plantations under DPTA, 1994 against tree felling permissions issued in various projects :

- Total **139.5 ha** of land has been handed over by DDA to Forest Department, Delhi for the purpose in phases during the period w.e.f. 2014 to 2020 for plantation purpose.
- In **139.5 ha** of land **1,70,876** saplings have been planted by Forest Department, Delhi.

(iii) **Details of plantations carried out as Compensatory Afforestation against the Forest land diverted under Compensatory Afforestation Act (FCA), 1980:**

- Total **105.368 ha** of land has been handed over by DDA to Forest Department, Delhi for the plantation purpose in phases during the period w.e.f. 2014 to 2021.
- Out of **105.368 ha** land, **102.418 ha** of land has been afforested with **1,29,002** plant saplings by Forest Department, Delhi.

(iv) **Plantation during World Forestry Day, 2023:**

- 83,593 plants and 4,50,000 grass have been planted in 5 km stretch of DDA Land from Garhi Mandu to Shastri park near Yudhister setu along Yamuna Flood Plains (Not handed over to Forest Department).
 - Plantation of 1,805 saplings on island 1, 2, and 3.
 - Plantation of 1,400 saplings at Shastri Park Metro Station.
 - Plantation of 2,500 saplings at Garhi Mandu track.
 - Plantation of 3,333 saplings at Garhi Mandu walkway.
 - Plantation of 450 saplings around pond near wazirabad near Signature Bridge.
 - Plantation of 7000 saplings along Yamuna path.

(v) **Details of Plantation carried out under State during 2024-25:**

- Plantation of 17100 Bamboo has been carried out at NH-24 Plantation sites (5 ha, 2.41 ha, 6.13 ha, 12.00 ha 1.81 ha).
- Plantation of 55000 Bamboo and 7000 shrubs at Garhi Mandu and Shastri Park Metro Station Plantation area has been carried out.
- Plantation of 2000 trees and 15000 shrubs are carried out at ITO Chungi Loops & Parts.

(vi) **Details of Plantation carried out under DPTA during 2024-25:**

- Plantation of 25550 trees are carried out at Old Garhi Mandu Safeda Patch.
- Plantation of 14000 trees at Garhi Mandu Pocket B& D and 4000 at Pocket A & E.

- | |
|--|
| <ul style="list-style-type: none">• Total land handed over till date = 629.468 ha• The area that has been afforested till date = 626ha• Total no. of saplings planted= 7,80,793• Total no. of grass planted= 4,50,000 |
|--|

XX. Development of Biodiversity Park (on Yamuna Flood Plain) :

- **Yamuna Biodiversity Park is already existing** and located in Jagatpur Khadar Yamuna Flood Plains in 9770 Hectares (upstream of Wazirabad).
- **Kalindi Biodiversity Park** (Between DND to proposed Kalindi Bypass on Western Bank) is being developed by Delhi Development Authority in the 115 Hectares area in Yamuna Flood Plains. The project has been awarded to CEMDE on 13.12.2019. Three out of 11 Wet Lands are completed in available space. Further work is held up due to NHA work. DJB is initiating a project to tap the drains.

XI. Details of Reuse of Treated Waste Water and the details of tanker deployment by various stake holders departments for the month of April, 2025 is at Annexure -11.

XXII. Model River being adopted by the State & Action Proposed for achieving the bathing quality standards:

In case of Delhi there is only one river i.e. Yamuna river and efforts are being made to comply with the directions of Hon'ble NGT in OA No. 673/2018, OA No. 06/2012 in the matter of Manoj Mishra Vs. Union of India & others and OA 21/2023 in the matter of Ashwani Yadav Vs. Govt. of NCT of Delhi [Now OA No. 06/2012 (Nizamuddin West Association Vs Union of India & Ors)] .

In absence of minimum Environmental Flow of river Yamuna in Delhi it is very difficult to achieve the bathing quality standards.

XXIII. Status of Preparation of Action Plan by the Coastal States : Not applicable in case of Delhi

XXIV. Regulation of Mining Activities in the State/UT: Not applicable in case of Delhi

XXV. Action against identified polluters, law violators and officers responsible for failure for vigorous monitoring:

DPCC takes action against the violating Industries/ Units including Water Polluting Industries /Units and imposes Environmental Compensation (EC) on the Polluter Pays Principle regularly.

A Joint Team consisting of MCD, DPCC, Revenue Dept., Power Companies, DJB has been constituted for taking action taken against Dyeing units in non-conforming areas of Delhi.

Inspections are carried out by the said Joint Team and action taken since 01.05.2023 till 07.05.2025 is briefed below:

- No. of Dyeing Industries/ Units Closed down / Sealed / Electricity Disconnected : 208

DPCC has also issued directions on 22.06.2023 to Local Bodies, DDA, DJB & Discoms (BSES/ NDPL) for closure / sealing & disconnection of Electricity and Water Supply of all Dyeing units and Jeans /Denim washing units operating outside the Approved Industrial Areas /Industrial Estates / Redevelopment Areas or operating without mandatory consent of DPCC.

Details of the Operational STPs of Delhi Jal Board and Compliance Status w.r.t. Prescribed standards in April., 2025

S.No.	Name of STP	Capacity (in MGD)	Capacity being utilized (in MLD)	Capacity being utilized(in MGD)	Design Parameters BOD/TSS (in mg/l)	Date of Sampling	Compliance status [Prescribed standards by DPCC : [(pH 6.5 - 9.0), TSS $\leq$ 10 mg/l],(BOD $\leq$ 10 mg/l),(COD $\leq$ 50mg/.) ,(Ammonical Nitrogen $\leq$ 5mg/l),(Total Nitrogen $\leq$ 10 mg/l), (Phosphate (PO ₄ - P) $\leq$ 2 mg/l) (Fecal Coliform (FC){MPN / 100ml}<230)]
1.	Mehrauli	5	21	4.619	20/30	10.04.2025	Not meeting the prescribed standards in respect of TSS (39 mg/l), BOD (16 mg/l), COD(60mg/l)and Fecal Coliform (2500 MPN/100ml).
2.	Okhla Phase -V	16	68	14.958	30/50	09.04.2025	Not meeting the prescribed standards in respect of TSS (14 mg/l) and BOD (12 mg/l) and Fecal Coliform 350 MPN/100ml).
3.	Okhla Phase -VI	30	118	25.957	20/30	09.04.2025	Meeting the prescribed standards
4.	Molar Band	0.66	2.2	0.484	30/50	09.04.2025	Not meeting the prescribed standards in respect of TSS (34 mg/l) and BOD (36 mg/l), COD (120 mg/l) and Fecal Coliform (2700MPN/100ml).
5.	Sen Nursing Home Nallah	2.2	11	2.420	10/15	23.04.2025	Meeting the prescribed standards
6.	Vasant Kunj (Old) Phase-I	2.2	7	1.540	30/50	10.04.2025	Not meeting the prescribed standards in respect of TSS (45 mg/l), BOD (36 mg/l) , COD (136 mg/l) and Fecal Coliform (9100MPN/100ml).
7.	Vasant Kunj (New) Phase-II	3	8	1.760	30/50	10.04.2025	Not meeting the prescribed standards in respect of TSS (37 mg/l), BOD (36 mg/l), COD (116 mg/l) and Fecal Coliform (21000 MPN/100ml).
8.	Ghitorni	5	12	2.640	30/50	10.04.2025	Not meeting the prescribed standards in respect of TSS (28 mg/l), BOD (40 mg/l), COD (160 mg/l) and Fecal Coliform (22000 MPN/100ml).
9.	Delhi Gate Nallah (Old) Phase-I	2.2	11	2.420	10/15	23.04.2025	Meeting the prescribed standards.
10.	Delhi Gate Nallah (New) Phase-II	15	65	14.298	10/10	23.04.2025	Meeting the prescribed standards.
11.	Kondli Phase - I	10	46	10.119	10/10	23.04.2025	Meeting the prescribed standards
12.	Kondli Phase - II	25	91	20.018	10/10	23.04.2025	Meeting the prescribed standards (Under test and trial run)
13.	Kondli Phase - III	10	46	10.119	10/10	23.04.2025	Meeting the prescribed standards
14.	Kondli Phase - IV	45	198	43.555	10/10	23.04.2025	Not meeting the prescribed standards in respect of TSS (12 mg/l), BOD (13 mg/l) and Fecal Coliform (3500 MPN/100ml).
15.	Chilla	9	41	9.019	10/10	23.04.2025	Meeting the prescribed standards

Details of the Operational STPs of Delhi Jal Board and Compliance Status w.r.t. Prescribed standards in April., 2025

S.No.	Name of STP	Capacity (in MGD)	Capacity being utilized (in MLD)	Capacity being utilized(in MGD)	Design Parameters BOD/TSS (in mg/l)	Date of Sampling	Compliance status [Prescribed standards by DPCC : [(pH 6.5 - 9.0), TSS $\leq$ 10 mg/l) ,(BOD $\leq$ 10 mg/l) ,(COD $\leq$ 50mg/.) ,(Ammonical Nitrogen $\leq$ 5mg/l) ,(Total Nitrogen $\leq$ 10 mg/l), (Phosphate (PO ₄ - P) $\leq$ 2 mg/l) (Fecal Coliform (FC){MPN / 100ml}<230)]
16.	Yamuna Vihar Phase-I	10	46	10.119	30/50	21.04.2025	Not meeting the prescribed standards in respect of TSS (14 mg/l), BOD (16mg/l) and Fecal Coliform (930 MPN/100ml).
17.	Yamuna Vihar Phase-II	15	67	14.738	30/50	21.04.2025	Meeting the prescribed standards.
18.	Yamuna Vihar Ph-III	25	119	26.177	20/30	21.04.2025	Not meeting the prescribed standards in respect of TSS (11 mg/l), BOD (16 mg/l)and Fecal Coliform (1200 MPN/100ml). .
19.	Akshardham / Common Wealth Games Village	1	0.5	0.110	02/01	23.04.2025	Meeting the prescribed standards.
20.	Coronation Pillar Phase- I&II	20	45	9.899	30/50	04.04.2025	Not meeting the prescribed standards in respect of COD (60 mg/l) and Fecal Coliform (540 MPN/100ml).
21.	Coronation Pillar Phase- III	10	38	8.359	30/50	04.04.2025	Not meeting the prescribed standards in respect of Fecal Coliform (460 MPN/100ml).
22.	New Coronation Pillar	70	160	35.196	10/10	04.04.2025	Meeting the prescribed standards (Under Test and Trial Run).
23.	Narela	15	41	9.019	30/50	22.04.2025	Not Meeting the prescribed standards in respect of TSS BOD (12 mg/l) and Fecal Coliform (350 MPN/100ml)
24.	Rithala Phase -II	40	173	38.055	15/20	11.04.2025	Meeting the prescribed standards.
25.	Rohini	25	90	19.798	30/50	11.04.2025	Not Meeting the prescribed standards in respect of TSS (14 mg/l), BOD (12 mg/l) and Fecal Coliform (430 MPN/100ml).
26.	Keshopur Phase - I (New)	12	53	11.659	20/30	04.04.2025	Meeting the prescribed standards.
27.	Keshopur Phase-II	20	92	20.238	30/50	04.04.2025	Meeting the prescribed standards.
28.	Keshopur Phase - III	40	148	32.556	30/50	04.04.2025	Meeting the prescribed standards.

Details of the Operational STPs of Delhi Jal Board and Compliance Status w.r.t. Prescribed standards in April., 2025

S.No.	Name of STP	Capacity (in MGD)	Capacity being utilized (in MLD)	Capacity being utilized(in MGD)	Design Parameters BOD/TSS (in mg/l)	Date of Sampling	Compliance status [Prescribed standards by DPCC : [(pH 6.5 - 9.0), TSS $\leq$ 10 mg/l) ,(BOD $\leq$ 10 mg/l) ,(COD $\leq$ 50mg/.) ,(Ammonical Nitrogen $\leq$ 5mg/l) ,(Total Nitrogen $\leq$ 10 mg/l), (Phosphate (PO ₄ - P) $\leq$ 2 mg/l) (Fecal Coliform (FC){MPN / 100ml}<230)]
29.	Nilothi Phase-I	40	98	21.557	30/50	17.04.2025	Not Meeting the prescribed standards in respect of Fecal Coliform (540 MPN/100ml).
30.	Nilothi Phase-II	20	90	19.798	10/10	17.04.2025	Meeting the prescribed standards
31.	Pappankalan Phase - I	20	72	15.838	30/50	17.04.2025	Not meeting the prescribed standards in respect of Fecal Coliform (9500 MPN/100ml).
32.	Pappankalan Phase - II	20	102	22.437	10/10	17.04.2025	Meeting the prescribed standards
33.	Najafgarh	5	23	5.059	30/50	17.04.2025	Meeting the prescribed standards
34.	Kapashera	5	23	5.059	10/10	10.04.2025	Meeting the prescribed standards
35.	Rithala Phase-I	40	168	36.956	10/10	11.04.2025	Meeting the prescribed standards. (Under Test and Trial Run)
36.	New Okhla STP	124	387	85.130	10/10	09.04.2025	Meeting the prescribed standards (Under trial run)
37.	Sonia Vihar	7	3	0.660	10/10	21.04.2025	Not meeting the prescribed standards in respect of TSS (14 mg/l), BOD (12 mg/l), COD (76 mg/l) and Fecal Coliform (320 MPN/100ml). (Under Test and Trial Run).
	Total	764.26* MGD	2783.7 MLD	612.341 MLD			

Note:-

1. DPCC Water Laboratory collected the samples from the inlet & outlet of 37 Operational STPs of Delhi Jal Board in the month of April, 2025.
2. As per the Analysis Reports of DPCC Water Laboratory for April, 2025, 21 STPs were found meeting the standards prescribed by DPCC and 16 STPs were found not meeting the standards prescribed by DPCC.

Upgradation/ Augmentation of Existing STPs**(Interventions –for Existing STPs to achieve BOD: TSS 10/10)****[Integrated Fixed Film Activated Sludge, Increased Aeration, Disc Filter, UV Disinfection & Odour Control]**

S. No.	Name of STP	Existing Capacity (In MGD)	Enhanced Capacity (In MGD)	Status	Timelines
1.	Rithala Phase –II	40	40	Completed & Under Trial Run	Completed and included in total capacity of 764 MGD along with New Okhla STP and Sonia Vihar New STP
2.	Kondli Phase-IV	45	45		
3.	Rohini Sector 25	15	25		
4.	Narela	10	15		
5	Najafgarh	5	5		
6	Coronation Pillar Phase -I & II	20	20		
7	Coronation Pillar Phase –III	10	10		
8	Keshopur Phase –II	20	20		
9	Keshopur Phase-III	40	60	95%	Revised Timeline to be informed.
10	Pappan Kalan Phase-I	20	30	74%	June-2025
11	Nilothi Phase –I	40	60	56%	Sept-2025
12	Okhla Phase- V	16	16	STPs is functional on existing parameters as BOD/TSS 20/30 mg/l. Tender for up-gradation and capacity augmentation shall be called after approval from the Apex Committee, since the Project is funded by GOI under AMRUT 2.0.	Dec-2026
13	Mehrauli	5	7.5		
14	Ghitorni	5	7.5	The STPs is functional on existing parameters as BOD/TSS 30/50 mg/l. Tender for up-gradation and capacity augmentation shall be called after approval from the Apex Committee, since the Project is funded by GOI under AMRUT 2.0.	
15	Vasant Kunj	5	7.5		
16	Yamuna Vihar Phase– I	10	15		
17	Keshopur Phase- I	12	18		
18	Yamuna Vihar Phase- III	25	55		June, 2027
	Total	343	456.5	Addition of 98.5 MGD by December-2026.	

Information about 22 Drains out falling into River Yamuna in Delhi, their Water Quality in April, 2025 and Proposed Action for Tapping of Flow

S.No.	Drain Owning Agency	Name of Drain	Flow in MLD (As per DJB)	Water Quality of Drain (As per DPCC Lab Report for Sample Taken on 07.04.2025)				Point of Sampling (Before Outfall into river) (Latitude , Longitude*)	Status of Drain (Tapped / Partially Tapped / Untapped)	STP in which tapped waste water is treated / proposed to be treated		Proposed Action / Timeline for Tapping of Drain
				pH (5.5 -9)	TSS (mg/l) (100)	COD (mg/l) (250)	BOD (mg/l) (30)			Name of STP	End Point of Disposal of Treated waste water from STP	
1	MCD	Metcalf House Drain	17.25 (3.79 MGD)	No Flow				28.6803991, 77.2291258	Tapped	Tapped waste is treated in Okhla STPs.	Agra canal	Drain already tapped.
2		Khyber Pass Drain	1.7 (0.37 MGD)	No Flow				28.6953254, 77.2279064	Tapped			Drain already tapped
3		Sweeper Colony Drain	8.6 (1.89 MGD)	No Flow				28.6900959, 77.2282293	Tapped			Drain already tapped
4		Magazine Road Drain	7.8 (1.72 MGD)	No Flow				28.6977573, 77.2274876	Tapped			Drain already tapped
5		Tonga Stand Drain	7.8 (1.72 MGD)	No Flow				28.6629212, 77.2407143	Tapped			Drain already tapped
6		Civil Mill Drain	14.68 (3.23 MGD)	No Flow				28.6507572, 77.2525033	Tapped			Drain already tapped
7		Moat Drain (Vijay Ghat)	-	Dry				-	Tapped			Dry Drain (Already Tapped)
8		Drain No.14	25.87 (5.69 MGD)	No Flow				28.6115925, 77.2517744	Tapped			Drain already tapped
9		Tehkhand Drain	39.74 (8.74 MGD)	No Flow					Tapped			Drain already tapped
10		Tuglakabad Drain (Kalka Ji Drain merged in this drain)	25.05 (5.51 MGD)	7.1	436	356	115	28.5419317, 77.3082674	Untapped	Okhla STPs.	Agra canal	DJB has informed that this drain is catering the discharge of Tugalkabad, Tehakhand area and falls in Agra Canal. This drain has been tapped at Sarita Vihar SPS near Mathura Road from where it is pumped to Okhla STP for Treatment. However, flow observed by DPCC Lab on 24.04.2024, 03.06.2024, 04.09.2024 , 08.10.2024, 06.11.2024 , 10.01.2025, 10.02.2025, 05.03.2025& 07.04.2025.

S. No.	Drain Owning Agency	Name of Drain	Flow in MLD (As per DJB)	Water Quality of Drain (As per DPCC Lab Report for Sample Taken on 07.04.2025)				Point of Sampling (Before Outfall into river) (Latitude , Longitude*)	Status of Drain (Tapped / Partially Tapped / Untapped)	STP in which tapped waste water is treated / proposed to be treated		Proposed Action/ Timeline for Tapping of Drain
				pH (5.5 -9)	TSS (mg/l) (100)	COD (mg/l) (250)	BOD (mg/l) (30)			Name of STP	End Point of Disposal of Treated waste water from STP	
11	MCD	Abul Fazal Drain	7 (1.54 MGD)	7.8	91	260	90	28.5458359, 77.2982617	Untapped	Proposed to be treated in Okhla STP.	Agra canal	This drain is catering the discharge of Canal Colony of UP Irrigation and un-tapped sewer connections of Abul Fazal Enclave. The un-tapped sewer connections have been started and likely to be completed by 31.05.2025. After tapping of un-tapped sewer connections, the flow in the drain shall be reviewed. If the sewage flow exist in the drain then a tapping shall be constructed and flow will be diverted to peripheral sewer line to Okhla STP. Timeline : August, 2026.
12	MCD	Sen Nursing Home Drain	43.20 (9.5 MGD)	7.1	132	232	86	28.6205472, 77.2516466	Partially tapped	Partially tapped waste water is treated in Sen Nursing Home STP, remaining to be treated in Okhla STP.	Yamuna River (From Sen Nursing Home STP) Agra canal from Okhla STP.	Overflow / un-tapped waste water will be treated at Okhla STP after tapping into Ring Road Trunk Sewer. Timeline: December, 2025
13		Delhi Gate Drain / Power House Drain	122.58 (26.96 MGD)	7.2	166	240	90	28.6350404, 77.255442	Partially tapped	Partially tapped waste water is treated in Delhi Gate STPs remaining to be treated in proposed New STP at Delhi Gate	Yamuna River	There are 2 operational STPs of 68.2 MLD & 10MLD for treatment of tapped waste water of this drain. Another STP of 45.46 MLD (10 MGD) is proposed for Treatment of remaining untapped waste water of this drain. Possession of land taken by DJB on 03.04.2025. 650 trees to be shifted. Permission for shifting of trees is in process. Estimate is under approval. STP will be constructed within 18 months after award of work. Alternatively, consultant is being appointed for preparation of DPR etc. to explore possibilities of construction of 15 MGD STP in place of existing 2.2 MGDSTP at Delhi Gate. Timeline: June, 2027

S. No.	Drain Owning Agency	Name of Drain	Flow in MLD (As per DJB)	Water Quality of Drain (As per DPCC Lab Report for Sample Taken on 07.04.2025)				Point of Sampling (Before Outfall into river) (Latitude , Longitude*)	Status of Drain (Tapped / Partially Tapped / Untapped)	STP in which tapped waste water is treated / proposed to be treated		Proposed Action/ Timeline for Tapping of Drain
				pH (5.5 -9)	TSS (mg/l) (100)	COD (mg/l) (250)	BOD (mg/l) (30)			Name of STP	End Point of Disposal of Treated waste water from STP	
14		ISBT Drain (Qudsia Bagh/ Mori Gate Drain)	43.2 (9.51 MGD)	7.2	162	216	74	28.6694576, 77.2336664	Untapped	Proposed to be treated in New Coronation Pillar STP	Najafgarh Drain	For Mori gate STP, an alternative proposal is framed to sewage to Coronation Pillar STP for its treatment via Nehru Vihar SPS by laying a rising main from SPS(18MGD) at ISBT Kashmere Gate. Work Order was issued on 23.12.2022. and likely completed by June, 2025. Laying of Rising main work is held up due to unavailability of road/land cutting permissions from PWD/IFC/MCD/ DDA , further for partial tapping of the drain, it is to be connected to Bella road trunk sewer that would be treated at Okhla STP which is under approval. An site inspection by DG (NMCG), CEO (DJB), CEN(Dr) it is proposed to construct STP at the mouth of the drain before discharging into river Yamuna at flood plain to tap it. Work is in progress
15	MCD	Sonia Vihar Drain (On Eastern Bank of Yamuna)	27.24 (5.99 MGD)	7.0	146	144	60	28.7084002, 77.2360452	Untapped	Sonia Vihar STP (under construction)	Yamuna River	Sonia Vihar drain outfalls into Sonia Vihar Pond. The complete discharge from the pond has been tapped and treated in newly constructed 7MGD Sonia Vihar STP. It's effluent is being discharged into River Yamuna through outlet chamber of Sonia Vihar WTP However DPCC Lab observed Flow during visit on 10.01.2025, 10.02.2025, 05.03.2025& 07.04.2025.
16		Kailash Nagar Drain (On Eastern Bank of Yamuna)	13.62 (3.0 MGD)	7.2	274	224	56	28.6640877, 77.2494362	Untapped	Proposed to be treated in Kondli STP	Yamuna River	Feasibility of diverting the flow of the drain to Kondli STP through Geeta Colony and Preet Vihar SPS is being worked out jointly with MCD, DUSIB, DDA and DJB. Tapping is to be done by providing house sewer connections in the vicinity of the drain to the existing DJB sewerage system. During

												the inspection of DG NMCG on 24.04.2025, DSTP is proposed at mouth of the drain to tap it before discharge into river Yamuna. Timeline: June, 2027
17		Shastri Park Drain (On Eastern Bank of Yamuna)	5.45 (1.2 MGD)	No Flow				28.6621096, 77.2546735	Untapped	Proposed to be treated in DSTP.	Yamuna River	Partially tapped by DJB, finally going into Buland Masjid SPS. Feasibility of construction of DSTP is being worked out jointly with MCD, DUSIB, DDA and DJB. Tapping is to be done by providing 1200 nos approx house sewer connections in the vicinity of the drain to the existing DJB sewerage system. Estimate of House sewer connection framed by maintenance division is under approval. During the inspection of DG NMCG on 24.04.2025, DSTP is proposed at mouth of the drain to tap it before discharge into river Yamuna. Timeline: June, 2027
18		Barapulla Drain	145.15 (31.97 MGD)	7.0	107	332	110	28.5831727, 77.2640264	Untapped	Proposed to be treated in Okhla STP.	Agra canal	Work of Intercepting the Barapullah drain flow by laying of interceptor sewer through micro tunnelling and conveying the flow to Okhla STP for treatment is in progress and expected to be completed by June, 2025.
19		Maharani Bagh Drain	30.24 (6.65 MGD)	7.3	352	580	180	28.5723966, 77.2686193	Untapped	Proposed to be treated in Okhla STP.	Agra canal	The work of tapping has been completed to partially trap the flow to the extent of 9-10 MLD in C.V. Raman Marg Trunk sewer. The balance flow of the Maharani Bagh drain will be tapped in the proposed scheme of Barapullah drain. The construction of I&D structure for trapping of Maharani Bagh Drain is held-up due to Hon'ble Delhi High Court and widening of Maharani Bagh Drain is under progress under the STF constituted by Delhi High Court.. Timeline: December, 2025.

20		Jaitpur Drain	5.68 (1.25 MGD)	No Flow				28.5419379, 77.3083086	Untapped	Proposed to be treated Okhla STP.	Agra canal	This drain is catering the discharge of NTPC, Ali Gaon, Madanpur Khadar and Jaitpur unsewered area and falls under Madanpur Khadar GOC & Tajpur Pahari/ Badarpur GOC. In Madanpur Khadar GOC 03 colonies (out of 07 colonies) and in Tajpur Pahari/ Badarpur GOC 56 Colonies (out of 83 colonies) falls under O-Zone. After laying the sewerage network the flow sewage of these colonies shall be treated at Okhla WWTP and propose 10 MGD DSTP at Tajpur Pahari. be diverted to peripheral sewer line. STP is required to be constructed at the mouth of the drain.
S. No.	Drain Owning Agency	Name of Drain	Flow in MLD (As per DJB)	Water Quality of Drain (As per DPCC Lab Report for Sample Taken on 07.04.2025)				Point of Sampling (Before Outfall into river) (Latitude , Longitude*)	Status of Drain (Tapped / Partially Tapped / Untapped)	Proposed Action/ Timeline for Tapping of Drain		
				pH (5.5 -9)	TSS (mg/l) (100)	COD (mg/l) (250)	BOD (mg/l) (30)					
21	Irrigation & Flood Control Deptt.	Najafgarh Drain	2056.32 (452.34 MGD)	7.3	116	192	76	28.7090142, 77.2286028	Being large drain not feasible to be tapped However covered under ISP for tapping the flow of its Sub Drains	There is about 453 MGD flow in the Najafgarh drain. Out of this at present 252 MGD comprises of treated effluent from STPs. From Haryana, untreated discharge of 105 MGD is being discharged through Badshahpur and DD-6 drains. There are 126 sub-drains out falling in Najafgarh Drain including Supplementary drain. Out of 126 sub-drains, 20 sub-drains are un-trapped and these will be trapped in June,2025. The balance 5 sub-drains which depend upon availability of land and 2 sub-drains are related to DDA. There are 110 sub-drains out falling in Supplementary drain. Out of 110 sub-drains, about 01 sub-drains are un-trapped and balance one will be trapped as estimate for installation of DSTP has been prepared and NIT yet to be floated due to budget constraints.		
22		Shahdara Drain	475.2 (104.66 MGD)	7.0	384	268	92	28.5588984, 77.3207987	Being large drain not feasible to be tapped However covered under ISP for tapping the flow of its Sub Drains	Total discharge in Shahdara drain is about 105 MGD, out of which 50 MGD (i.e., 45%) is untreated sewage is being discharged by UP through Sahibabad, Indirapuri and Banthala drain. There are 230 sub-drains out falling in Najafgarh Drain including Shahdara drain. Out of 230 sub-drains, 2 sub-drains are untapped, and these will be trapped by June, 2025.		
			3411.6 (750.4MGD)									

Brief Status of Common Effluent Treatment Plants (CETPs) in Delhi
(Based on the Analysis Reports of DPCC Laboratory for the Month of April, 2025)

Annexure -4

S. No.	Name of CETP	Industrial Areas Connected with CETP	Capacity (in MLD)	Monthly Average Flow (in MLD)	Date of Sampling	Influent Quality at Inlet (in mg/l)	Effluent Quality at Outlet (in mg/l)	Compliance Status w.r.t Prescribed Standards.
1	Jhilmil CETP	Jhilmil and Friends Colony Indl. Area	16.8	4.326	16.04.2025	pH - 7.4 TSS – 532 COD - 520 BOD - 180 Oil & Grease – 37.6 Ammonical Nitrogen (N) – 9.1 Phosphate- 14.3 Sulphide – 2.9	pH - 7.2 TSS - 32 COD - 84 BOD - 27.5 Oil & Grease – 5.2 Ammonical Nitrogen (N) – 1.5 Phosphate- 5.0 Sulphide – 2.0	Meeting the Prescribed Standards.
2	Badli CETP	Badli Industrial Estate	12	2.418	11.04.2025	pH - 6.9 TSS - 272 COD - 424 BOD - 140 Oil & Grease – 14 Ammonical Nitrogen (N) – 3.9 Phosphate- 0.8 Sulphide – 3.8	pH - 7.3 TSS - 64 COD - 112 BOD - 27 Oil & Grease – 7.6 Ammonical Nitrogen (N) – 0.5 Phosphate- 0.1 Sulphide – 1.6	Meeting the Prescribed Standards.
3	Mayapuri CETP	Mayapuri Indl. Area	12	3.75	15.04.2025	pH - 7 TSS – 272 COD - 448 BOD - 150 Oil & Grease – 12 Ammonical Nitrogen (N) – 8.2 Phosphate- 4.3 Sulphide – 3	pH - 7.4 TSS - 76 COD - 100 BOD - 28 Oil & Grease – 5.2 Ammonical Nitrogen (N) – 4 Phosphate- 0.6 Sulphide – 1.9	Meeting the Prescribed Standards.

Brief Status of Common Effluent Treatment Plants (CETPs) in Delhi
(Based on the Analysis Reports of DPCC Laboratory for the Month of April, 2025)

Annexure -4

S. N o.	Name of CETP	Industrial Areas Connected with CETP	Capacity (in MLD)	Monthly Average Flow (in MLD)	Date of Sampling	Influent Quality at Inlet (in mg/l)	Effluent Quality at Outlet (in mg/l)	Compliance Status w.r.t Prescribed Standards.
4	Mangolpuri CETP	Mangolpuri Indl. Area	2.4	1.47	15.04.2025	pH - 6.9 TSS - 260 COD - 440 BOD - 140 Oil & Grease – 19.2 Ammonical Nitrogen (N) – 11.9 Phosphate-7.6 Sulphide – 2.5	pH - 7.4 TSS - 90 COD - 96 BOD - 27.5 Oil & Grease –9.6 Ammonical Nitrogen (N) – 1.6 Phosphate- 0.6 Sulphide – 1.6	Meeting the Prescribed Standards.
5	Wazirpur CETP	Wazirpur Indl Area	24	4.456	22.04.2025	pH – 6.6 TSS - 172 COD - 408 BOD - 130 Oil & Grease –16 Ammonical Nitrogen (N) – 7.5 Phosphate-2.3 Sulphide – 2.3	pH -7.3 TSS - 96 COD - 140 BOD - 34 Oil & Grease – 3.6 Ammonical Nitrogen (N) – 2.9 Phosphate-1.2 Sulphide – 0.3	Exceeding the Prescribed Standards.
6	Nangloi CETP	Nangloi& Udyog Nagar Indl Areas	12	3.492	15.04.2025	pH -7.3 TSS - 456 COD - 480 BOD - 160 Oil & Grease – 10.4 Ammonical Nitrogen (N) – 15.2 Phosphate-8.6 Sulphide – 3.2	pH -7.2 TSS - 82 COD - 116 BOD - 28 Oil & Grease – 1.6 Ammonical Nitrogen (N) – 6.5 Phosphate-0.5 Sulphide – 1.4	Meeting the Prescribed Standards.

Brief Status of Common Effluent Treatment Plants (CETPs) in Delhi
(Based on the Analysis Reports of DPCC Laboratory for the Month of April, 2025)

Annexure -4

S. No.	Name of CETP	Industrial Areas Connected with CETP	Capacity (in MLD)	Monthly Average Flow (in MLD)	Date of Sampling	Influent Quality at Inlet (in mg/l)	Effluent Quality at Outlet (in mg/l)	Compliance Status w.r.t Prescribed Standards.
7	SMA CETP	SMA, Rajasthani Udyog Nagar and SSI Industrial Areas	12	2.7	16.04.2025	pH - 6.2 TSS - 504 COD - 408 BOD - 170 Oil & Grease – 26.4 Ammonical Nitrogen (N) –5.8 Phosphate-10.7 Sulphide – 3.1	pH -7.1 TSS - 44 COD - 68 BOD - 24 Oil & Grease – 3.2 Ammonical Nitrogen (N) – 1.5 Phosphate- 2 Sulphide – 1.6	Meeting the Prescribed Standards.
8	Okhla CETP	Okhla Indl. Area	24	2.25	09.04.2025	pH - 7.1 TSS - 508 COD - 664 BOD - 210 Oil & Grease – 16.4 Ammonical Nitrogen (N) – 12.8 Phosphate- 10.3 Sulphide – 3.8	pH - 7.3 TSS - 64 COD - 144 BOD - 36 Oil & Grease – 1.2 Ammonical Nitrogen (N)– 3.3 Phosphate – 2.0 Sulphide – 1.8	Exceeding the Prescribed Standards.
9	Narela CETP	Narela Indl. Area	22.5	8.661	22.04.2025	pH - 6.8 TSS – 472 COD - 528 BOD - 170 Oil & Grease – 29.6 Ammonical Nitrogen (N) –9.4 Phosphate-1.6 Sulphide – 2.5	pH – 7.4 TSS - 84 COD - 104 BOD - 32.5 Oil & Grease – 6.4 Ammonical Nitrogen (N) – 1.8 Phosphate- 0.2 Sulphide – 1.4	Exceeding the Prescribed Standards.
10	Bawana CETP	Bawana Indl. Area	35	30.69	22.04.2025	pH - 6.6 TSS - 508 COD - 552 BOD - 180 Oil & Grease – 20.8 Ammonical Nitrogen (N) – 8.6 Phosphate- 5.6 Sulphide – 3.4	pH -7 TSS - 50 COD - 96 BOD - 28 Oil & Grease –2 Ammonical Nitrogen (N) –2.7 Phosphate- 0.6 Sulphide – 1.1	Meeting the Prescribed Standards.

Brief Status of Common Effluent Treatment Plants (CETPs) in Delhi
(Based on the Analysis Reports of DPCC Laboratory for the Month of April, 2025)

Annexure -4

S. No.	Name of CETP	Industrial Areas Connected with CETP	Capacity (in MLD)	Monthly Average Flow (in MLD)	Date of Sampling	Influent Quality at Inlet (in mg/l)	Effluent Quality at Outlet (in mg/l)	Compliance Status w.r.t Prescribed Standards.
11	Naraina CETP	Naraina Indl. Area	21.6	5.33	15.04.2025	pH - 6.8 TSS - 160 COD - 344 BOD - 125 Oil & Grease - 6.8 Ammonical Nitrogen (N)- 10.9 Phosphate- 5.4 Sulphide - 2.7	pH - 7.3 TSS - 50 COD - 64 BOD - 26 Oil & Grease -8.4 Ammonical Nitrogen (N) - 1.6 Phosphate - 0.4 Sulphide - 1.3	Meeting the Prescribed Standards.
12	GTK CETP	GTK Road Indl. Area	6	2.13	16.04.2025	pH - 7.4 TSS - 412 COD - 424 BOD - 150 Oil & Grease -28.8 Ammonical Nitrogen (N)- 8.6 Phosphate- 2.1 Sulphide -4.5	pH - 7.1 TSS - 72 COD - 124 BOD - 32 Oil & Grease -4.8 Ammonical Nitrogen (N)-3.9 Phosphate-1.1 Sulphide - 1.6	Exceeding the Prescribed Standards.
13	Lawrence Road CETP	Lawrence Road Indl. Area	12	1.746	22.04.2025	pH - 6.7 TSS - 264 COD - 432 BOD - 130 Oil & Grease - 16.4 Ammonical Nitrogen (N)- 8.2 Phosphate- 2.3 Sulphide - 2.8	pH - 7 TSS - 94 COD - 88 BOD - 30 Oil & Grease - 2.4 Ammonical Nitrogen (N)- 2.2 Phosphate- 0.3 Sulphide - 1.4	Meeting the Prescribed Standards.
		Total	212.3	73.419				

Existing & Proposed Municipal Solid Waste Processing Facilities in Delhi (As on 30.04.2025)**Total Municipal Solid Waste (MSW) Generation– 11342 TPD**

[MCD- 11000 TPD, NDMC- 280 TPD, DCB- 62 TPD]

S.No.	MSW Processing Facility	Capacity (in TPD)	Processing of fresh MSW (in TPD)
1.	Waste to Energy Plant at Okhla	1950 [MCD – 1550 + 400 (NDMC & DCB)]	1541.12*
2.	Waste to Energy Plant at Ghazipur	1300 (MCD)	543.1*
3.	Integrated MSW Facility at Bawana (1300 TPD Waste to Energy Plant & 700 TPD Compost Plant)	2000 (MCD) (As per Consent of DPCC)	2274*
4.	Waste to Energy Plant at Tehkhand	2000 (MCD)	1414.85*
5.	20 Composters of 1 TPD each	20 (MCD)	20
6.	05 Bio-Methanation / Bio- Gas Plants in NDMC Area	7.0 (NDMC)	2.5
7.	27 Organic Waste Convertors (OWCs) in NDMC Area	10 [NDMC]	5.0
8.	05 Community Composting in NDMC Area	5.0 [NDMC]	5.0
9.	Home Composting (~ 900 House Holds)	1.0 [NDMC]	1.0
10.	257 Compost Pits [MCD-211+ NDMC- 46 + DCB - 0]	558 [MCD – 543 + NDMC- 15 + DCB-0]	558 [MCD – 543 + NDMC- 15 +DCB-0]
Total		7851	6364.6
11	Recycling through 176 MRFs [MCD– 157 + NDMC- 08 +DCB-11]	322 TPD [MCD- 260 (42+218) + NDMC–12+ DCB - 50]	Recycling - 306 TPD [MCD - 260+ NDMC - 12+ DCB – 34]
Grand Total (in TPD) [Processing Fresh MSW+Recycling]		8173 TPD (72.06 %)	6670.6 TPD (58.8%)
12	Disposal of Fresh MSW at the Dumpsites	4671.4 TPD (41.2 %) [11342 TPD – 6364.6 TPD (Fresh MSW Processed) - 306 TPD (Recycled through MRFs)]	

*Based on the information provided by the 4 operators of the Waste to Energy Plants in Delhi.

Generati on (in TPD) (1)	Total Capacity of Existing MSW Processi ng Facilities +MRF(in TPD) (2)	Processing of Fresh MSW+ MRF (in TPD) (3)	Gap in Processing Capacity (in TPD) (4) = (1)-(2)	Gap in Processing (in TPD) (5)= (1)-(3)	Additional Proposed Capacity of Facilities (in TPD)				Total Capacity of MSW Processing Facilities + MRFs (in TPD)			
					By 2025	By 2026	By 2027	By 2028	By 2025	By 2026	By 2027	By 2028
11342	8173 (72.06 %)	6670.6 (58.84%)	3169 (27.94%)	4671.4 (41.2%)	400	750	2750	7750	8573 (75.6 %)	8923 (78.7%)	10923 (96.3%)	15923** (140.4%)

** will take care possible increase of MSW till year 2031.

Proposed MSW Processing Facilities of MCD in Delhi

S. No.	MSW Facility	No	Location	Capacity Addition (in TPD)	Timeline for Completion
1	New Waste to Energy Plant at Narela –Bawana (For 3 Zones City SP, Karol Bagh & Narela Zone)	1	Narela-Bawana	3000	November, 2028 The LOA to the successful bidder was issued on 06.01.2025 and the concession agreement signed on 27.02.2025. As per the Concession Agreement, a period of 270 days is allotted for fulfilling the conditions precedent by both the Concessionaire and MCD before the commencement of work. During this period, the concessionaire is required to obtain Environmental Clearance, and MCD must hand over a clear site to the Concessionaire after relocating the transmission lines of Powergrid and DTL. MCD will likely to make payment to Powergrid by end of May 2025. As per agreement with Powergrid, the time of 18 months is required to complete the shifting work. However, as per discussion with Powergrid officials, the work is likely to be completed by end of March 2026. Thereafter, duration of 24 months is provided for the setting up of the WTE (Waste-to-Energy) plant. The Concessionaire has applied for Environmental Clearance (EC) from the MoEF&CC, Govt. of India. The Terms of Reference (ToR) were issued on 10.01.2024, and the Public Hearing was conducted at the project site on 27.12.2024. The EC is currently awaited. A request letter for issuing the EC expeditiously has been sent to Secretary, MoEFCC on 06.05.2025.
2	New Waste to Energy Plant at Ghazipur	1	Ghazipur	2000	December, 2028 MCD has finalized the tender documents and filed a petition before DERC seeking approval of the bidding process prior to inviting tenders. The petition was filed before DERC in June 2023, and the matter was last heard on 01.05.2025. Upon receiving approval from DERC, MCD will be in a position to invite tenders. After inviting tenders, approx. 3 years would be required for completing tendering process and setting up of WTE plant. A land parcel of 15 acres is also required to be reclaimed at Ghazipur dumpsite through biominning.
3	Expansion of Existing Waste to Energy Plant at Okhla	1	Okhla	1000 (From 1950 TPD to 2950 TPD)	March, 2027 EC for expansion accorded on 09.03.2023 and DERC has accorded the approval of revised tariff on 09.07.2024. However, tariff decided by DERC is at variance with the tariff decided for WTE project at Narela Bawana. Accordingly, Department has taken a conscious decision to proceed further for expansion project of Okhla WTE by providing VGF as directed by DERC in their order dated 09.07.2024. This may facilitate lower or at par Tariff for the consumer. The terms & conditions of the supplementary agreement are being finalized. A request letter for VGF amounting to INR 50 Crores has been sent to GNCTD. After signing of the supplementary agreement, 18 months time would be required for commissioning of the plant
4	Expansion of Existing Waste to Energy Plant at Tehkhand	1	Tehkhand	1000 (From 2000 TPD to 3000 TPD)	December 2027 Approval accorded by the Corporation and conveyed to the Concessionaire. The Concessionaire has filed application for ToR on 28.10.2024 in MoEFCC. TOR is yet to be issued by MoEFCC. After obtaining EC, the Concessionaire will approach to DERC for tariff determination. Thereafter, a supplementary agreement will be signed
5	Bio CNG Plant	1	Okhla	300 (In place of existing Closed Compost plant of 200 TPD to 300 TPD)	July, 2025
6	Compressed Bio Gas (CBG) Plant	1	Ghogha Dairy	100	June, 2025
7	Compressed Bio Gas (CBG) Plant	1	Ghazipur	350	December, 2026 (Change of Land Use is awaited from DDA)
	Total	7		7750 TPD	
8.	Bio Gas Plants for Dairies Waste* Management	1	Nangli Dairy	215	December, 2025
		1	Goyla Dairy	215	December, 2025
		1	Ghogha Dairy	290	December, 2025
9.	Engineered Sanitary Landfill (SLF)	1	Tehkhand		Commissioned on 12.03.2024

*These Plants are mainly for waste generated from Dairies & not included in total MSW Generation of 11000 TPD of MCD.

Status of Bio-Mining of Legacy Waste at 3 Dumpsites (As on 02.05.2025)

S. No.	Dumpsite	Quantity of Legacy Waste Dumped (July, 2019) (Lakh Ton)	Total Quantity of Legacy Waste Bio-mined (Since Oct, 2019 to 02.05.2025) (Lakh Ton)	Legacy Waste (Volumetric Assessment through Drone Survey in June, 2022) (Above Ground) (Lakh Ton)	Quantity of Fresh MSW dumped from July 2022 to 02.05.2025 (Lakh Ton)	Total Quantity of Legacy Waste Bio-mined from July, 22 to 02.05.2025 (Lakh Ton)	Balance Quantity of Waste at Dumpsite (Lakh Ton)	Revised Timeline for 100% Remediation
1.	Bhalaswa	80	79.70 (99.63%)	73	29.36	55.36	47.00	Dec, 2027*
2.	Ghazipur	140	29.07 (20.76%)	85	17.20	18.50	83.70	Sept., 2028*
3.	Okhla	60	55.56 (92.60%)	45	22.18	37.98	29.20	March, 2028*
	Total	280	164.33 (58.69%)	203	68.74	111.84	159.90	

*Subject to the stoppage of incoming fresh waste and formation of Standing Committee in MCD.

Segregation of Waste at Source


NDMC – About 92% (in all 14 Circles).

DCB - 90% in Civil Pockets & 70 % in Army Pockets (100 % segregation at source by June, 2025).

MCD --- 60 % (Average)

(Timelines for segregation : 75 % by Aug., 2025, 85% by Feb., 2026, 90 % by Aug., 2026 & 100% by January, 2027)

No. of Zero Waste Colonies / Institutes – 633.

**WATER QUALITY STATUS OF RIVER YAMUNA**

REPORT NO: DPCC/W/Y/2025/01-08/1786
 DATE OF SAMPLING: 07.04.2025

Dated: 23/4/2025

S. No.	Sampling Locations	Latitude Longitude	pH	COD (mg/l)	BOD (mg/l)	DO (mg/l)	Fecal Coliform MPN/100ml	Phosphate (mg/l)	Ammonical Nitrogen (mg/l)
	Water Quality Criteria ('C' Class)		6.5-8.5	-	3mg/l or less	5mg/l or more	500 (desirable) 2500 (max permissible)	-	-
1	Palla	28.8138023, 77.2100181	7.9	32	4	5.4	22×10 ²	0.74	0.20
2	Wazirabad	28.7131310, 77.2319304	6.9	40	6	3.4	54×10 ²	0.84	0.65
3	ISBT Bridge	28.6713533, 77.2338207	7.1	104	33	NIL	22×10 ⁴	1.24	1.68
4	ITO Bridge	28.6284288, 77.2534977	7.2	144	40	NIL	28×10 ⁴	1.70	1.89
5	Nizamudin Bridge	28.5915608, 77.2715342	7.2	122	38	NIL	79×10 ³	1.64	1.76
6	Okhla Barrage	28°32'40 77°18'49	7.4	162	46	NIL	13×10 ⁴	1.57	2.28
7	Agra Canal at Okhla Barrage	28.545414, 77.311075	7.2	170	51	NIL	13×10 ⁴	1.77	2.16
8	River Yamuna at Asgarpur (After confluence of Shahdara & Tuglakabad drains)	28.4657003, 77.33905231	7.1	186	56	NIL	15×10 ⁵	1.92	2.36

Shweta
I/C Water Laboratory
Dr. Shweta Gupta
 Incharge (Water Laboratory)

[Signature]
SSA/Analyst



DELHI POLLUTION CONTROL COMMITTEE
WATER LABORATORY
 4thFLOOR, ISBT BUILDING, KASHMERE GATE, DELHI-06
 visit us at : <http://dpcc.delhigovt.nic.in>

WASTE WATER QUALITY STATUS OF DRAIN

REPORT NO: DPCC/W/D/2025/01-27/1787
 Date of Sampling: - 7/04/2025

dated: 23/4/2025

S.No.	Sampling location	pH	TSS (mg/l)	COD (mg/l)	BOD (mg/l)
	Standards	5.5- 9.0	100	250	30
1.	Najafgarh Drain	7.3	116	192	76
2.	Metcalfe House Drain	NO FLOW			
3.	Khyber Pass Drain				
4.	Sweeper Colony Drain				
5.	Magazine Road Drain				
6.	ISBT Drain	7.2	162	216	74
7.	Tonga Stand Drain	NO FLOW			
8.	Civil Mill Drain				
9.	SEN Nursing Home Drain	7.1	132	232	86
10.	Drain No. 14	NO FLOW			
11.	Power House Drain	7.2	166	240	90
12.	Indrapuri Drain	7.2	196	220	70
13.	Sonia Vihar Drain	7.0	146	144	60
14.	Kailash Nagar Drain	7.2	274	224	56
15.	Shastri Park Drain	NO FLOW			
16.	Barapulla Drain	7.0	107	332	110
17.	Maharani Bagh Drain	7.3	352	580	180
18.	Old Agra Canal Drain	NO FLOW			
19.	Jaitpur Drain				
20.	Sarita Vihar Pool	7.0	494	380	130
21.	Tuglakabad Drain	7.1	436	356	115
22.	Drain Near LPG Bottling Plant	NO FLOW			
23.	Drain Near Sarita Vihar Bridge (Mathura Road)				
24.	Shahdara Drain	7.0	384	268	92
25.	Sahibabad Drain	6.8	544	620	210
26.	Molarband Drain	TAPPED			
27.	Abul Fazal Drain	7.8	91	260	90

Shweta

I/C WATER LAB

Dr. Shweta Gupta
 Incharge (Water Laboratory)

[Signature]
SSA/Analyst

Status of 'Restoration and Rejuvenation of River Yamuna floodplains' as on 30th April 2025

ACTION TAKEN FOR PROTECTION OF LAND	
Demarcation of 1 in 25 year floodplains	591 Bollards erected at site; 375 Flag Posts have already been installed.
Signages	27. nos. of sign boards have been installed
Manual security	369 Security Guards have been deployed by DDA round the clock in three shifts at vulnerable points, with 3 patrolling vehicles in the Yamuna Flood Plain area from Wazirabad Barrage to Okhla Barrage to check illegal dumping of malba and to prevent encroachment. GPS monitoring of security guards & patrolling vehicles is being done.
Demolition programs	DDA has been carrying out demolitions to reclaim its land from encroachers. About 1536 acres of land is reclaimed in the past 2 years 3 months and more than 10500 Jhuggis/labor huts/semi- pucca structure, 25 religious structures, 7 dairy, 3 cricket, 200 cattle shed, 20 nurseries, 40 Bore well grounds have been Demolished.
Electronic surveillance system	90 No. CCTV cameras have been installed at 27 locations from Wazirabad Barrage to Okhla Barrage to check the illegal dumping of Malba in the Yamuna Flood Plain area.
Removal of C&D Waste	80,713 metric tonnes of C&D waste & 1160 metric tonnes of garbage lying in floodplain has been lifted to IL&FS site or utilized for development of Yamuna Project by DDA.

DETAILS OF CHALLANS FROM THE YEAR 2018-25

Sl. No.	Year	Offence	No. of challans	Compensation amount	Recovery amount
1.	2018	Dumping of malba	1	Rs.50,000/-	Nil
2.	2019	Dumping of malba, unauthorized parking and garbage dumping in Yamuna River flood plain.	186	Rs. 90,40,000/-	Rs.25,47,500/-
3.	2020	Dumping of malba and unauthorized parking in Yamuna River flood plain.	54	Rs.21,30,000/-	Rs.6,45,000/-
4.	2021	Dumping of malba and illegal parking in Yamuna River Flood Plain	776	Rs.1,22,95,000/-	Rs.23,70,000/-
5.	2022	Dumping of malba and illegal parking in Yamuna River Flood Plain	1167	Rs.2,75,25,000/-	Rs.32,96,000/-
6.	2023	Dumping of malba and illegal parking in Yamuna River Flood Plain	1255	Rs.1,29,80,000/-	Rs.14,20,000/-
7.	2024	Dumping of malba and illegal parking in Yamuna River Flood Plain	634	Rs.1,66,75,000/-	Rs.25,80,000/-
8.	2025	Dumping of malba and illegal parking in Yamuna River Flood Plain	63	Rs. 18,65,000/-	0
		TOTAL =	4136	Rs. 8,25,60,000/-	Rs.1,28,58,500/-

Through e-mail

**DELHI DEVELOPMENT AUTHORITY
OFFICE OF THE SUPTDG. ENGINEER, HCC-3
17TH FLOOR, VIKAS MINAR, I.P. ESTATE,
NEW DELHI -110002**

To

Sh. D.K. Singh,
Addl. Director, DPCC,
Deptt. of Environment, Govt. of NCT of Delhi,
5th floor, ISBT Building, Kashmere Gate.
Delhi -110006.

Sub:- Monthly progress report as on 30th April 2025 in reference to the order of Hon'ble NGT in OA No. 673/2018(Reg. Rejuvenation of River Yamuna).

Sir,

Kindly find enclosed herewith the monthly progress report as on 30th April 2025 in respect of projects taken up / to be taken up by DDA for development of Yamuna River Front for your kind perusal please.

Yours faithfully,



(Er. Rajnish Kumar)
SE/HCC-3/DDA

Encl: As above.

Copy to :

1. CE/Hort./DDA for kind information please (through email).
2. Smt. Kalpana Khurana, Addl. Comm.(LS), DDA for kind information please (through email).
3. EE/HCD-9&10 as per their report for kind information & n.a.
4. EE(P&HQ)/HCC-3 for kind information & n.a.



SE/HCC-3/DDA

Status of 'Restoration and Rejuvenation of River Yamuna floodplains' as on 30th April 2025

	Project	Area	Water bodies	Timelines	Status
1.	Asita East – (Old Railway Bridge to ITO Barrage - Eastern Bank) PART A: Under the jurisdiction of DDA .	PART A: 90 Ha	Part A: 1	Phase I: Completed	Initial proposal of development work is completely executed
				Phase II :	Further development work in progress.
	PART B: Under the jurisdiction of UP Irrigation Deptt. (Deposit work)	PART B:107 Ha	Part B: 3	Phase I: Completed	Initial proposal of development work is completely executed
				Phase II : 31/06/2025	Initial proposal of development work is completely executed Case No: SLP (C) 14342/2022 Case Title: Shakarpur Slum Union v/s DDA Court: Supreme court of India. Panel lawyer: Ms. Shalini Chandra & Mr. Sanjay Jain (ASG) Last Date of Hearing: 23.04.2025 & No stay
2.	KalindiAviral - (NH24 to DND Flyway- Western Bank)	Total Area : 100 Ha	3	Part A : Completed	Part A : Initial development work was completed but damaged by ongoing work of NCRTC.
	Kalindi Aviral Extension - (NH24 to DND Flyway- Western Bank)	Total Area : 163 Ha (i/c 12 Ha Baansera)		31/12/2026	Part A : Part of Restoration works have been damaged due to ongoing NCRTC works. NDOH:- 26/08/2025, 22/05/2025 26 Court Cases under 24(2) are pending in the Supreme Court of India. Part B: CLDP for entire 163 Ha has been issued. Detailed estimate of electrical , civil & horticulture has been complied and currently under scrutiny.
3.	Kalindi Biodiversity Park – (DND to proposed Kalindi By-Pass- Western Bank) Entrusted to CEMDE	115 Ha		Within 9 months after completion of NHAI project.	Project is being executed by CEDME. (Prof. C R Babu) 3 nos. Wetlands are completed in available space. Further work is held up due to NHAI work. DJB is initiating a project to tap the drains. A total of 35 cases are currently active in various courts (High Court, Saket Court) Case no: WP (C) 5822/2021, Last DOH:- 03/03/2025 (Disposed Off) Case no: CS(SCJ) 1352/2023, Last DOH:- 15/07/2024 Case no: WP (C) 15746/2023, Last DOH:- 03/02/2025 (Disposed Off)
4.	Yamuna Vatika (Asita West) - (Old Railway Bridge to ITO Barrage- Western Bank)	Part A : 93 Ha	Part A : 2	Part A:- Completed	Restoration work completed.
			Part B	Phase I: Completed	Initial proposal of development work is completely executed

Status of 'Restoration and Rejuvenation of River Yamuna floodplains' as on 30th April 2025

	Part A : 93 Ha (Already developed) Part B : 107 Ha (under development)	Part B : 107 Ha	: 5	Phase II : 30/06/2025	Works for Arrival Zone, Treatment zone and pathways in progress; treatment zones and pathways in progress Revised layout plan has been received and estimate has also submitted for approval accordingly. Case no: SLP(C) No. 9284/2023 Last date of hearing- 23.04.2025.
5.	Amrut Bio Diversity Park- ITO to NH-24 (Eastern & Western Bank)- Area South of CWG Village Area Part A : 90 Ha Part B : 18 Ha Part C : 8.25 Ha (Western bank) - CPWD	Part A : 90 Ha (Eastern bank)	6	PART A: Completed	Initial proposal of development work is completely executed. Inaugurated by Hon'ble L.G. on 7 th March 2025.
		Part B : 18 Ha (Western bank)		Part B :	Part B : Work can't be taken up due to stay by Delhi High Court
		Part C : 8.25 Ha		Part C :	Part C : Area handed over to CPWD (Nav Bharat Udyan)
6.	Ghat Area : Wazirabad to Old Railway Bridge- Western Bank Part A : Entrusted to INTACH (Qudsia Ghat)	Total Site Area- 66 Ha Qudsia Ghat- 16 Ha	1	Part A : Completed	Part A: Present progress is 99% (Civil) 81% (Hort.). Phase-I works Completed The work of parking in Akhada area is in progress. The tender awarding for restoration of Old ghat is in progress. Case no: RCA/SCJ 17/2022, Next DOH: -25.04.2025 Case no: HC/LM (32198)2018 W.P.(C)9342/2018, NDOH: 10.07.2025. Case no: CS No. 1191/23, Next DOH: Decision is pending & religious structure has been removed after approval of Religious Committee. Case no: Appt. No. 22/2023, Last DOH: 07.08.2025. Case no: W.P.(C)/3656/2024& CM Appl. 15121 /2024 & CM Appl. 15122 /2024, NDOH: 15.05.2025
	Part B : Sur ghat, Eco-trail, Yamuna Bazaar	Sur Ghat-13.6 Ha, Eco-trail- 33 Ha, Yamuna Bazaar Area- 3.4 Ha)		Part B : 30/06/2026	Development work is in progress at site. The work for the parking in eco-trail area is completed. The pedestrian track in eco trail area is completed.
7.	Yamuna Vanasthali- (Wazirabad Barrage to ISBT Bridge- Eastern Bank, around GarhiManduVillage&Usman pur Village)	236.5 Ha	7	Completed	Phase-I works Completed Minor repairing/ finishing works neat pushta no.-3 is completed Court Cases: 1) WP(C) 7542/ 2017; Last DOH- : 18.03.2025 (Disposed Off)

Status of 'Restoration and Rejuvenation of River Yamuna floodplains' as on 30th April 2025

8.	Mayur Nature Park- (NH-24 to DND Flyway- Eastern Bank) PART A: Under the jurisdiction of DDA . PART B: Under the jurisdiction of UP Irrigation Deptt.	Total Area- 397.75 Ha PART A: 235 Ha PART B: 162.75 Ha	----	31/10/2026	Drawing has been passed in SCM committee. Detailed drawings will be issued in phase wise manner The work of UP Irrigation land of 162.75 Ha is to be taken up on deposit work basis. Case no: W.P.(C)2504/23, Last DOH:-03.02.2025(Disposed Off) Case no: W.P.(C)7563/23, Last DOH:- 03.02.2025(Disposed Off)
9.	Eco-Tourism Area- (Geeta Colony Bridge to ITO Barrage- Western Bank)	30 Ha	---	Yet to be planned	Area falls outside the 1 in 25 year floodplain. Proposal will be taken up once the 'O-II' is finalized after notification of MPD-2041.
10.	Hindan Sarovar- (NH-24 to DND Flyway- Eastern Bank) Part Area-II- Hindon Cut Wetlands I&II PART A: Under the jurisdiction of DDA . PART B: Under the jurisdiction of UP Irrigation Deptt. (Deposit work)	Total Site Area- 53.6 Ha PART A: 15 Ha PART B: 30 Ha		31/10/2026	Proposal under progress.

Reuse of Treated STP Water

S.No.	Particular	Quantum in MGD
1	Quantum of Available Treated STP Water	612 (April, 2025)
2	Mandatory Return Flow in River Yamuna	267 (As per MOU of 1994)
3	Present Use of Treated STP Water	About 117 MGD For Horticulture in various parks in Delhi including Millennium Park in I.P Estate, Japanese Garden in Rohini, various parks in NDMC area , DTC Depots, PPCL , in Artificial Lakes / Water Bodies (Pappankalan, Nilothi & Najafgarh, Sanjay Van, Smriti Van Kondli & Sanjay Lake , Kondli, Dwarka)] developed by DJB.
4	Balance Available Treated STP Water	228 MGD
5	Proposed Use of Treated STP Water	Ground water recharge through lakes. NTPC Eco Park, Water bodies , supply to Farmhouses for Horticulture purpose etc

Number of Tankers Deployed

S.No.	Agency	No. of Tankers Engaged
1	CPWD	02
2	DDA	06
3	DJB internal Horticulture use	13
4	DTC	01
5	IL & FS	01
6	Forest	01
7	L&T	12
8	SMCD	03
9	NBCC	05
10	NHAI	02
11	North West MCD	01
12	Private Agencies	155
13	PWD	111
14	SDMC	25
15	EDMC	22
16	MCD	04
	TOTAL	368

Yamuna Rejuvenation

DELHI JAL BOARD


30.04.2025



River Yamuna.....



The Holy RIVER YAMUNA originates from the Yamunotri Glacier near Banderpoonch Peaks (6387 mtrs above MSL) in District Uttarkashi, Uttrakhand. It travels a total length of 1,376 kilometres and merges with the Ganges at Triveni Sangam, Prayagraj (Allahabad), Uttar Pradesh.

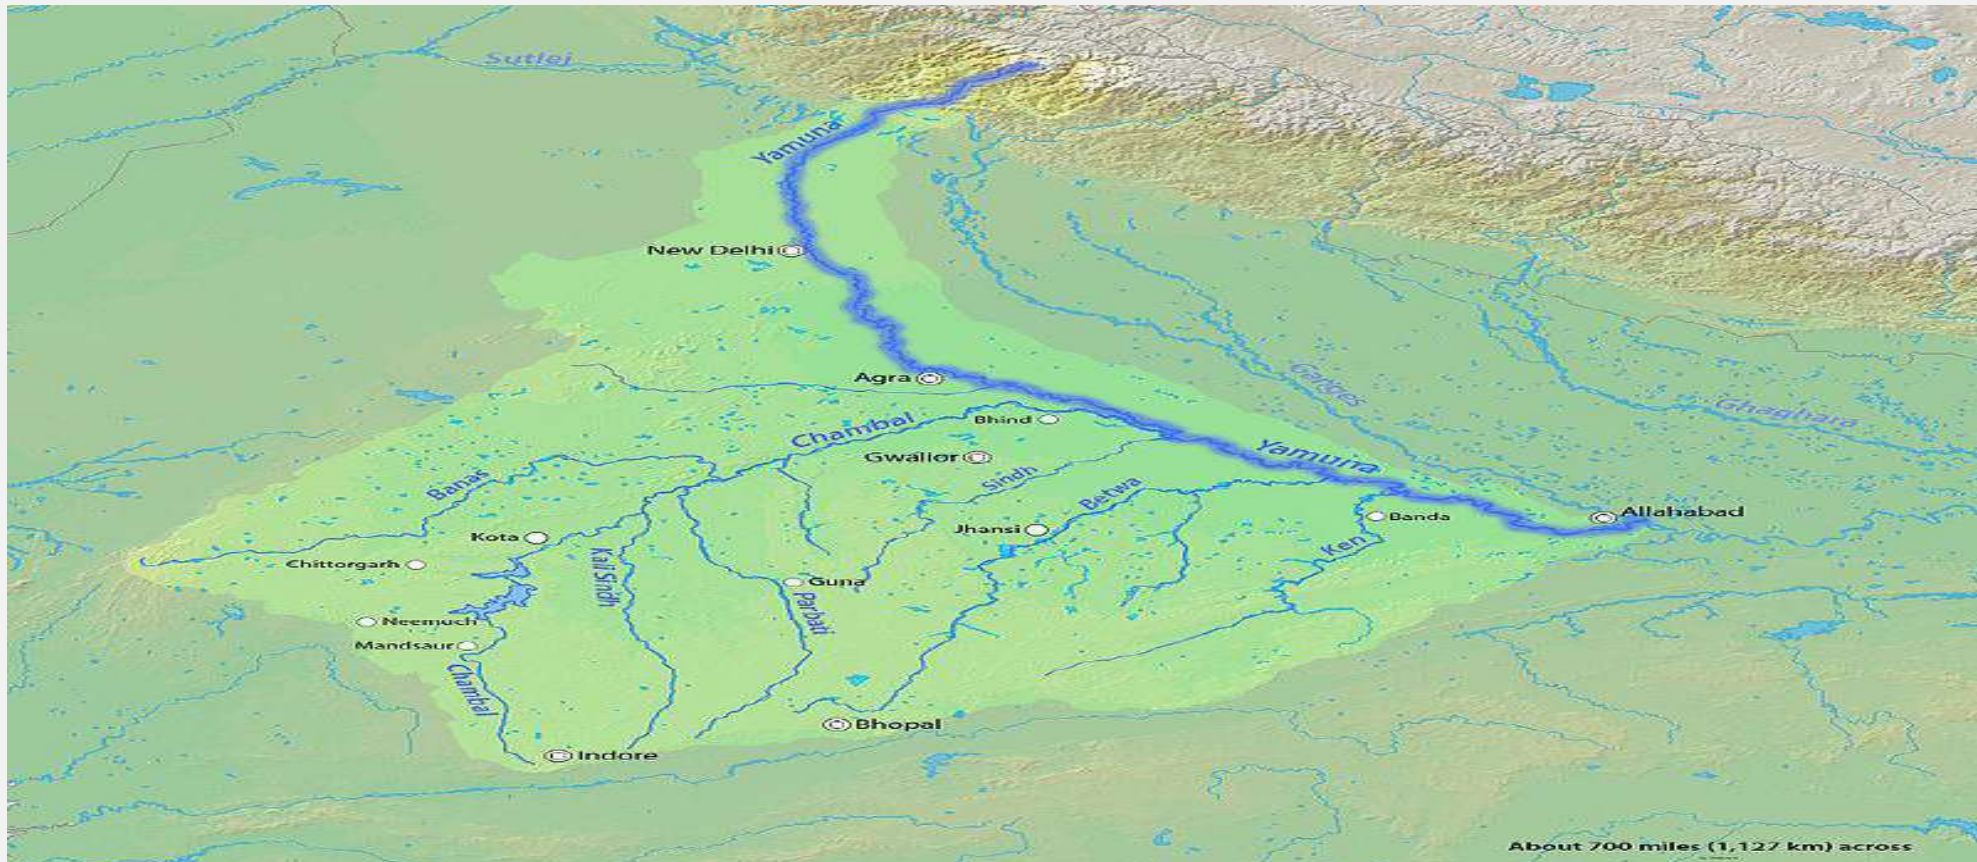

Schematic diagram depicting Yamuna's catchment



RIVER YAMUNA- SEGMENTS




Distinguished Independent Segments of River Yamuna

Segment	Limit of Segments	Approx Length(Km)
Himalayan Segment	From origin to Tajewala Barrage	172 kms
Upper Segment	Tajewala Barrage to Wazirabad Barrage	224 Kms
Delhi Segment	Wazirabad Barrage to Okhla Barrage	22 Kms
Eutrophicated Segment	Okhla Barrage to Chambal Confluence	490 kms
Diluted Segment	Chambal Confluence to Ganga Confluence	468 kms





Yamuna river in Delhi

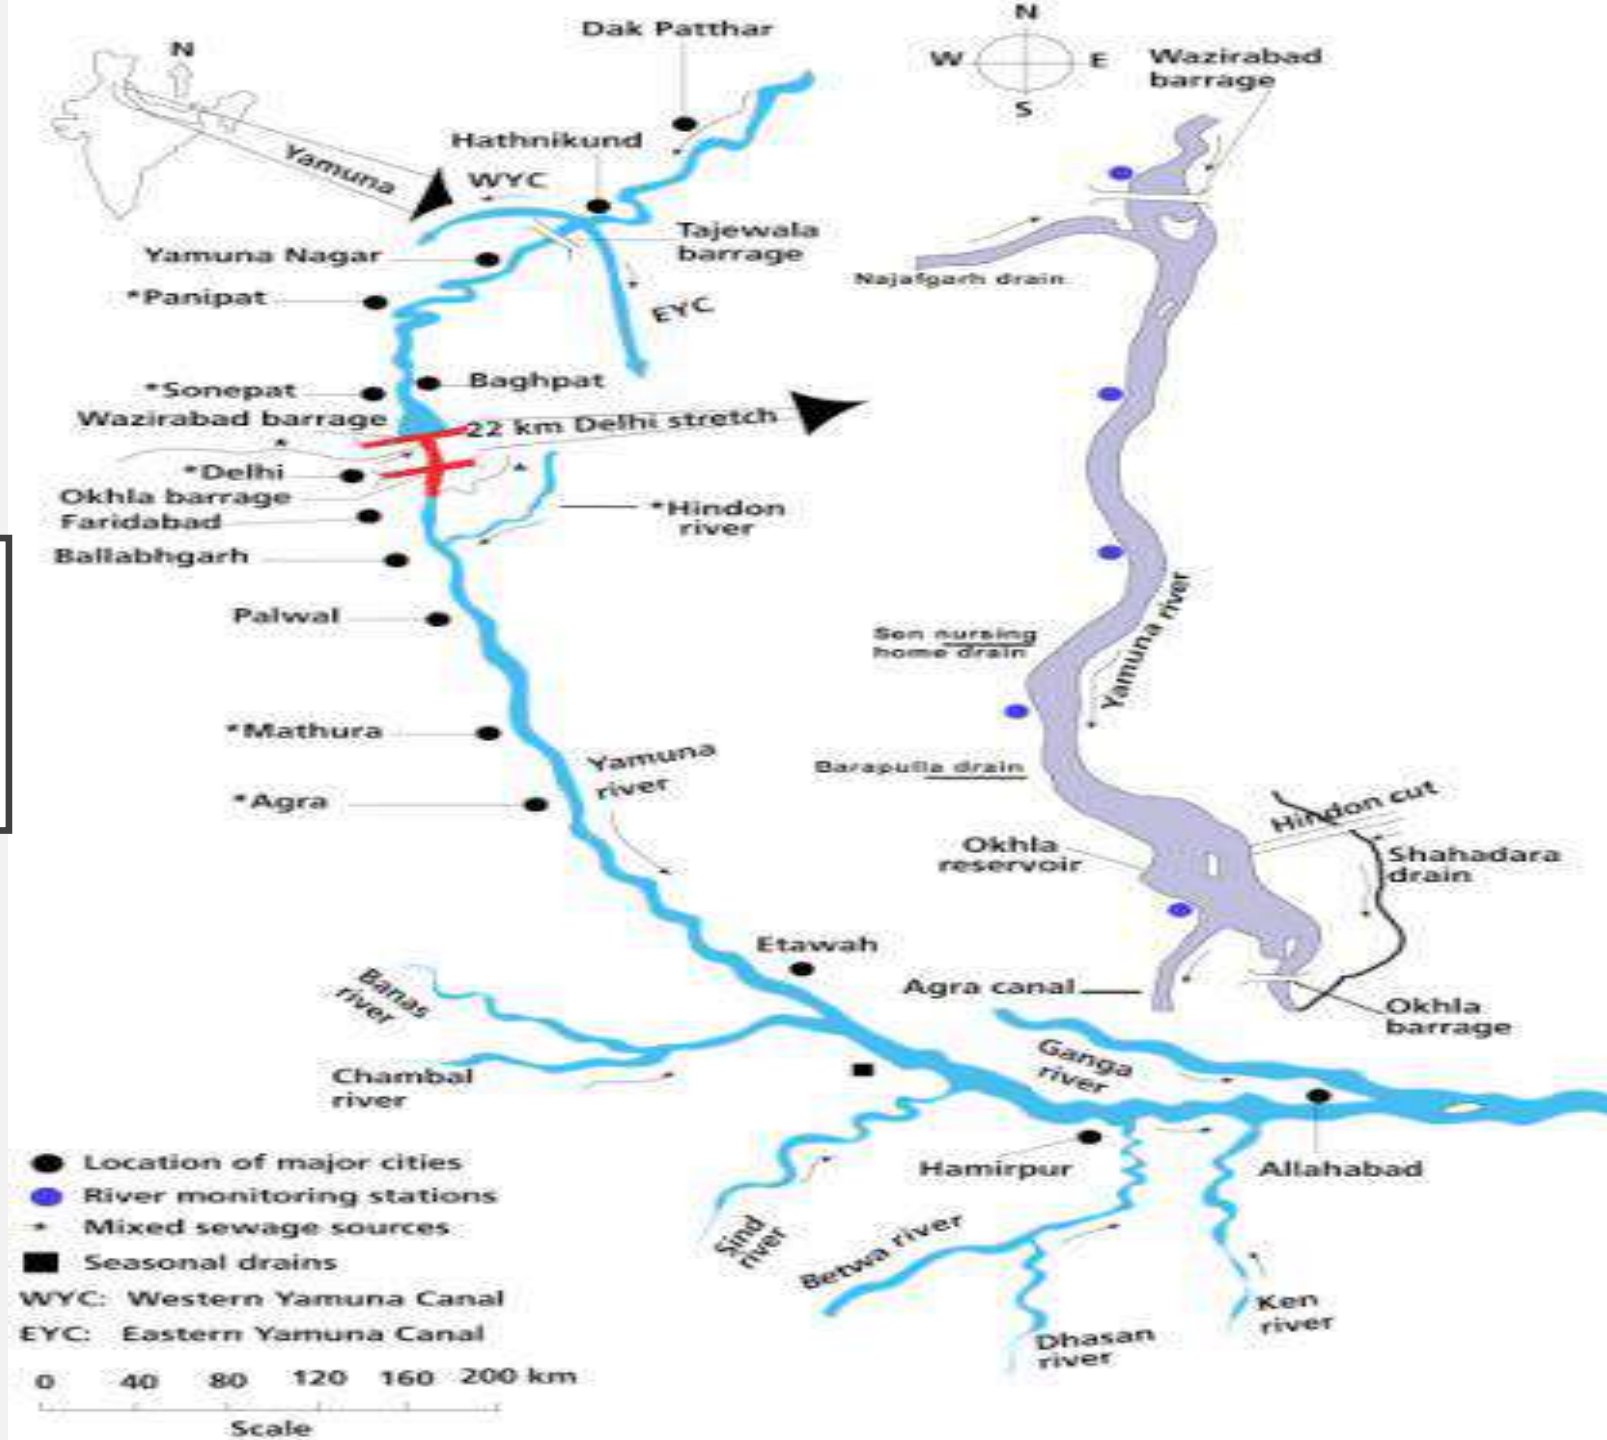

1. E-Flow in River Yamuna

Target – Sept., 2026

Treated Water from Coronation Pillar and Yamuna Vihar STPs (773 MLD) to be discharged into the river at Wazirabad downstream.

- A. Coronation Pillar STP :- National Mission for Clean Ganga (NMCG), Ministry of Jal Shakti, Gol appointed M/s. WAPCOS Limited to work out the feasibility and prepare the scheme accordingly for discharging treated effluent from Coronation Pillar STP to River Yamuna directly.
- B. Yamuna Vihar STP:- At present there is provision for discharging treated effluent from Yamuna Vihar STP into river Yamuna exists through effluent pumping station of 90 MGD capacity at Yamuna Vihar. One rising main of 1500 mm dia already discharging about 40 MGD treated effluent in River Yamuna. Estimate for laying of missing link of 2nd rising main of 1500 mm dia has been framed and processed for AA&ES as per guidelines issued from the UD Department, GNCTD.

2.2 Najafgarh and Shahdara ISP - Making all 6 existing packages functional and Assessment of overflows if any **Target – June, 2025**

S N	Name of Package & No	Design Capacity in MGD	Actual flow in MGD as on date	Name & Capacity of STPs in MGD	Overflows	Remark
1	Package-1 (Pappankalan)	13.83	0	Pappankalan Ph-1&2-40MGD	13 MGD	Presently, the total utilized capacity of Pappan Kalan STP is about 35 MGD as 20 MGD Ph- I is under upgradation. The treatment capacity shall be augmented from 40 to 50 MGD, which will be completed by June 2025. After the capacity augmentation of STPs, the interceptor flow will be treated. In addition to the flow coming from dedicated Sewer line through SPS other than ISP. For trapping entire flow from Palam drain, about additional 10 MGD Capacity STP will be required.
2	Package-2 Keshopur	64.12	35	Keshopur & Nilothe STPs-132MGD	29.12MGD	Presently, the total utilized capacity of Nilothe and Keshopur STPs is 132 MGD. The treatment capacity from 132 to 172 MGD, which will be completed by Sept-2025. After the capacity augmentation of STPs, the complete interceptor flow will be trapped. In addition to the flow coming from dedicated Sewer line through SPS other than ISP. There is performance issue on the part of M/s. PMC of ISP Package-2.
3	Package-3 Coronation & Rithala STPs	69.26	56	Coronation, Rithala STPs-180	0	ISP package-3 is functional and supplying 55-60 MGD to Coronation pillar STP through Burari ISP SPS and Rithala STP through Bharat Nagar SPS. There is adequate capacity at Coronation Pillar & Rithala STPs presently and treating entire incoming sewage. The package-3 is yet to be handover from EIL, However, the agency M/s. PMC is under Liquidation.

2.2 Najafgarh and Shahdara ISP - Making all 6 existing packages functional and Assessment of overflows if any **Target – June, 2025**

S N	Name of Package & No	Design Capacity in MGD	Actual flow in MGD as on date	Name & Capacity of STPs in MGD	Overflows	Remark
4	Package-4 Rohini STPs	25.9	18	Rohini STP-25MGD	0	10 MGD flow from Rithala ISP has been diverted at Rohini STP at present, however in future additional 20 MGD (approx.) treatment capacity will require to cater the flow of Kirari GOC/ Begampur GOC/Shabhad & Daulatpur GOC in near future. Rithala ISP SPS have the provision for pumping at Rithala and Rohini STPs,
5	Package-5 Yamuna Vihar STPs	30.9	0	Yamuna Vihar STPs-50MGD	30.9MGD	Presently, about 50 MGD generated from dedicated Sewer line of the command area is being treated against installed capacity of 50 MGD at Yamuna Vihar STPs. The Flow of about 30 MGD coming from ISP will be treated after upgradation and capacity augmentation of Yamuna Vihar Ph.-III(25 MGD) to 40 MGD and construction of new 15 MGD STP at Yamuna Vihar STP along with upgradation of Yamuna Vihar Ph- I from 10 to 15 MGD. In case of access flow in future DSTP is required to be constructed at certain drains as further space for expansion is not available at Yamuna Vihar.
6	Package-6 Kondli STPs	33.66	23	Kondli STPs-90MGD	6MGD	Presently, about 85 MGD is being treated against installed capacity of 90 MGD at Kondli STP. 2 nos drains (Kanti Nagar & Old Seelampur of approx. 6 MGD will be trapped by December-2025 and shall be treated at Kondli STP. Provision of diversion of flow from Kalyanpuri SPS to Chilla STP is also planned.

2.3 Litigation on contractual issues in Package II and III is to be resolved

Target – June, 2025

Interceptor Project- 2

- Work awarded to M/s. Pratibha Mosinzhstroi Consortium (PMC).
- The ISP Package was handover to DJB on 7.06.21 for 10 year O&M but the firm was under Liquidation.
- The Liquidator issued no objection towards Union Bank of India to enforce, realise, settle, compromise or deal with the Security Interest and compliance for *O&M works*.
- Union Bank of India has further handed over the project to M/s. Primus Insolvency Resolution and valuation private limited under Mr. Sanjay Gupta as Administrator to take control of the project.
- The Union Bank of India is not performing the O&M having several deficiencies as per term & conditions. Therefore DJB decided to issue Show Cause notice deemed fit as per Law.

2.3 Litigation on contractual issues in Package II and III is to be resolved

Target – June, 2025

Package -3

- Work awarded to M/s. Pratibha Mosinzhstroi Consortium (PMC).
- As per the Hon'ble High Court's directive, all deficiencies are to be addressed by May 2025 by M/S EIL being Project Management Consultant. Once these deficiencies are resolved, EIL will hand over the project to DJB.
- Due to dispute between M/S Pratibha Mosinzhstroi Consortium, RKC(Sub contractor) operation of Package-3 is affected and DJB is trying to resolve through EIL.


2.4 Abul Fazal, Jaitpur, Tughlaqabad drainage block (tapping)

Target – Aug, 2026

A. Abul Fazal Drain : This drain is catering the discharge of Canal Colony of UP Irrigation and un-trapped sewer connections of Abul Fazal Enclave. The un-trapped sewer connections have been started and likely to be completed by 31.05.2025. After trapping of un-trapped sewer connections, the flow in the drain shall be reviewed. If the sewage flow exist in the drain than a trapping shall be constructed and flow will be diverted to peripheral sewer line to Okhla STP.



B. Jaitpur Drain : This drain is catering the discharge of NTPC, Ali Gaon, Madanpur Khadar and Jaitpur unsewered area and falls under Madanpur Khadar GOC & Tajpur Pahari/ Badarpur GOC. In Madanpur Khadar GOC 03 colonies (out of 07 colonies) and in Tajpur Pahari/ Badarpur GOC 56 Colonies (out of 83 colonies) falls under O-Zone. After laying the sewerage network the flow sewage of these colonies shall be treated at Okhla WWTP and propose 10 MGD DSTP at Tajpur Pahari. be diverted to peripheral sewer line. STP is required to be constructed at the mouth of the drain.

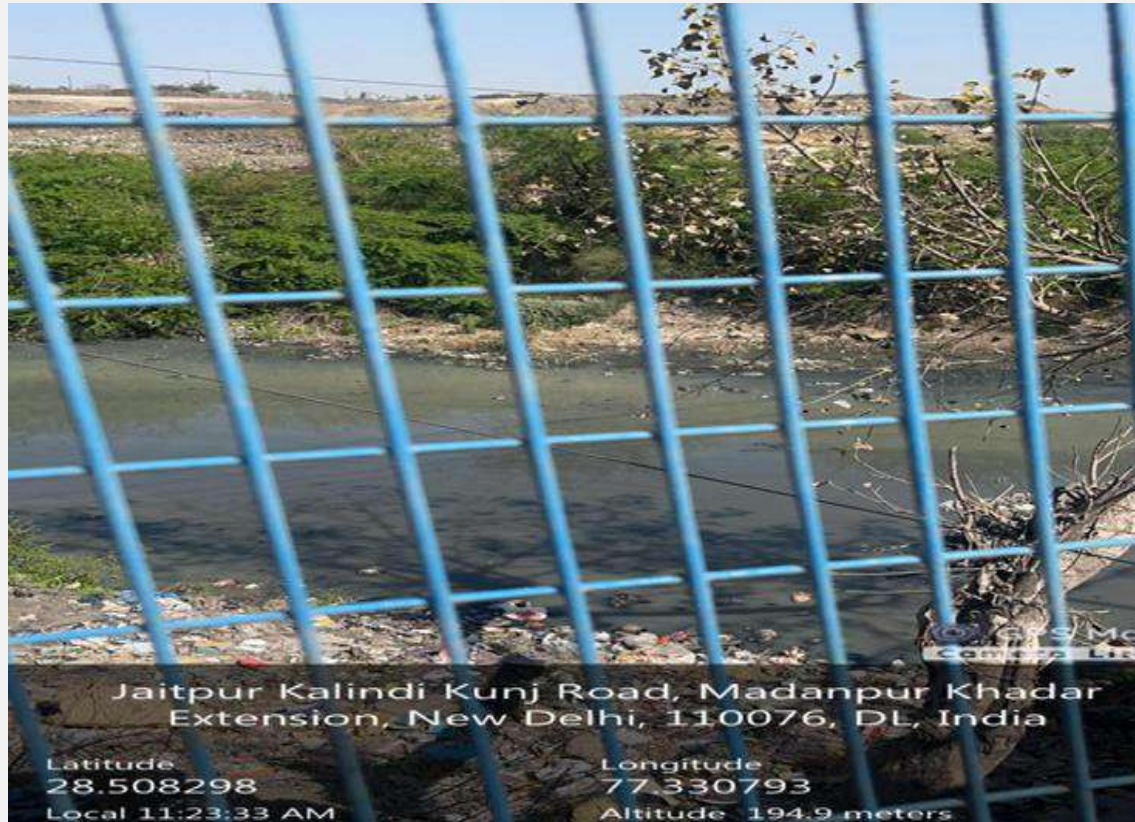

C.Tugalkabad Drain : This drain is catering the discharge of Tugalkabad, Tehakhand area and falls in Agra Drain. This drain has been trapped at Sarita Vihar SPS near Mathura Road.



2.5 Tapping of Barapullah, Maharani Bagh and Mori Gate Drain



(Maharani Bagh Drain)

The construction of I&D structure for trapping of Maharani Bagh Drain is held-up due to Hon'ble Delhi High Court and widening of Maharani Bagh Drain is under progress under the STF constituted by Delhi High Court.



(Mori gate drain)

Mori gate SPS having capacity of 18 MGD is almost completed. Laying of Rising main work is held up due to unavailability of road/land cutting permissions from PWD/IFC/MCD/DDA , further for partial trapping of the drain, it is to be connected to Bella road trunk sewer that would be treated at Okhla STP which is under approval. An site inspection by DG (NMCG), CEO (DJB), CEN(Dr) it is proposed to construct STP at the mouth of the drain before discharging into river Yamuna at flood plain to trap it.



2.6 Tapping of Balance Sub drains of Najafgarh drain and Shahadra drain

During the inspection of DG NMCG on 24.04.2025, it was suggested to construct STP/DSTP on the mouth of the drain to trap it fully before discharge into river Yamuna.

2.7 Tapping of Sonia Vihar, Delhi Gate, Kailash Nagar and Shashtri Park

Target – June, 2027

Shastri park drain

Shastri park drain have a discharge of about 1.5 MGD whose trapping is to be done by providing 1200 nos approx house sewer connections in the vicinity of the drain to the existing DJB sewerage system. Estimate of House sewer connection framed by maintenance division is under approval. During the inspection of DG NMCG on 24.04.2025, DSTP is proposed at mouth of the drain to trap it before discharge into river Yamuna.



2.7 Tapping of Sonia Vihar, Delhi Gate, Kailash Nagar and Shashtri Park

Target – June, 2027

Kailash nagar drain

Kailash nagar drain have a discharge of about 2.5MGD whose trapping is to be done by providing house sewer connections in the vicinity of the drain to the existing DJB sewerage system. During the inspection of DG NMCG on 24.04.2025, DSTP is proposed at mouth of the drain to trap it before discharge into river Yamuna.



Target – June, 2027



2.7 Tapping of Delhi Gate

Target – June, 2027

1. Possession of land taken over on 03.04.2025. There are about 650 trees which are to be shifted. Necessary permission for shifting of trees is in process.
2. Alternatively, consultant is being appointed for preparation of DPR etc. to explore possibilities of construction of 15 MGD STP in place of existing 2.2 MGD at Delhi Gate..

2.7 Tapping of Sonia Vihar, Delhi Gate, Kailash Nagar and Shashtri Park

Target – June, 2027

Sonia Vihar drain

Sonia Vihar drain have a discharge of about 1 MGD which outfalls in Sonia Vihar Pond. **The complete discharge from the pond has been trapped** at newly constructed Sonia Vihar STP & is being treated. It's effluent is being discharged into River Yamuna through outlet chamber of Sonia Vihar WTP.



7 MGD Sonia Vihar STP

2.7 Sonia Vihar Drain is trapped, pics of inspection by DG, NMCG on 24.04.2025




4. Sewage Management



- Delhi Jal Board has appointed M/s AECOM to prepare Sewerage Master Plan (SMP)-2031 for providing sewerage network in the entire Un-sewered areas of Delhi.
- The Approved SMP covers 1799 U/A colonies, unsewered Rural and Urban Villages.
- The approved SMP-2031 proposed to lay around 10000 km of the sewerage network , construction of 32 (Now 40+1) STPs/DSTPs and Augmentation of existing STPs.

4. SEWAGE MANAGEMENT.- SCENARIO IN DELHI

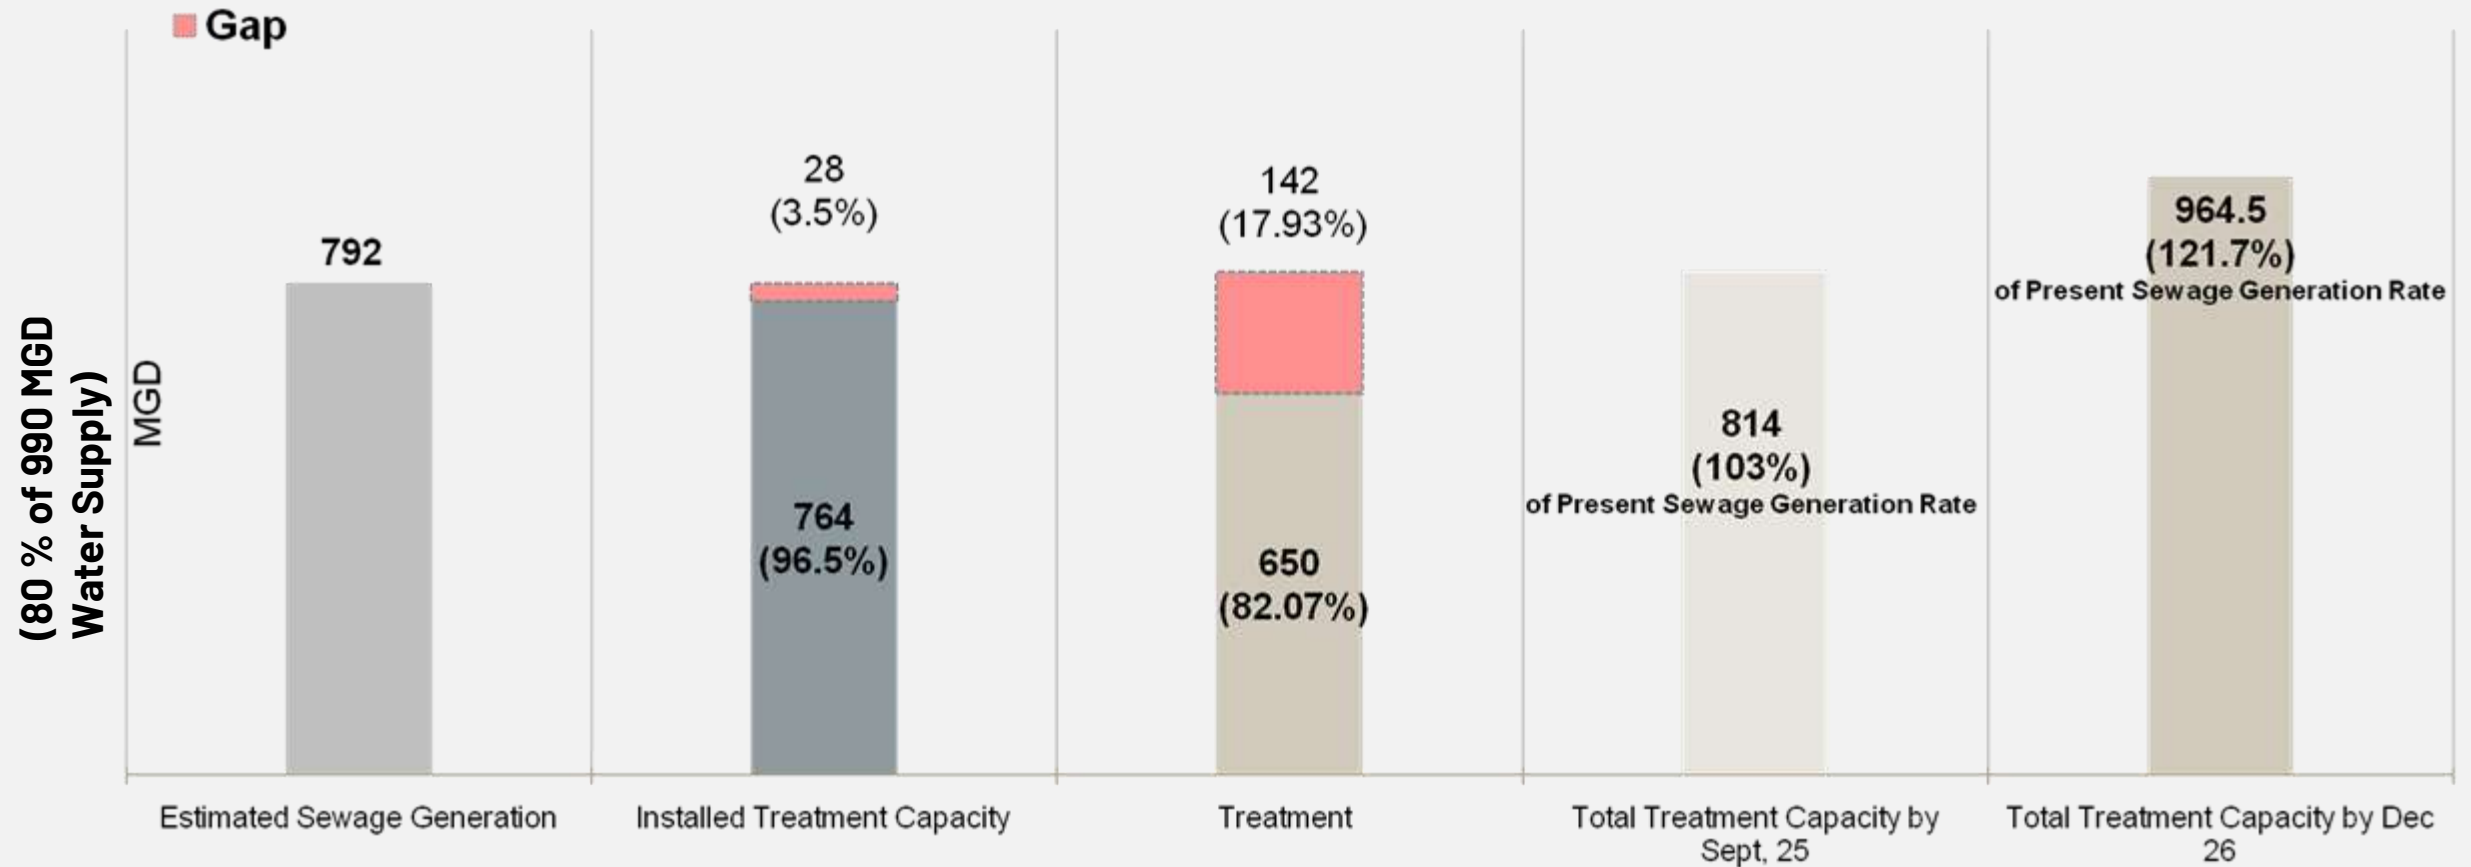

$$(764 - 964.5 \text{ MGD}) = 200.5 \text{ MGD}$$

4.1 Upgradation/ Capacity Augmentation of 5 STPs (225 MLD)

Target – June, 2026

Name of Contract packages	Interventions of existing STPs to achieve BOD:TSS 10/10 Increased aeration, Disc filter, UV Disinfection & Odor control			Status	Timelines
Package-1	Name of STP	Existing capacity	Enhanced capacity(In MGD)	- The STPs are functional on existing design parameters of 30/50 mg/l. However, plant is being upgraded on the design parameters of 10/10 mg/l for which 65% work already completed. - Pappankalan Ph-I of 30 MGD capacity is likely to complete by June-2025 and Nilothi Ph-I of 60 MGD capacity shall be completed by 30.09.2025	Sept-2025
	Pappan Kalan Ph-1	20	30		
	Nilothi Ph-1	40	60		
Package-2	Najafgarh	5	5	- The upgradation work of 5MGD Najafgarh STP has been complete and achieving the prescribed standards of DPCC. - The STPs are functional on existing design parameters of 30/50 mg/l. However, plant is being upgraded on the design parameters of 10/10 mg/l. Physical work of upgradation is completed and plant is under stabilization.	Completed
	Keshopur Ph-II	20	20		
	Keshopur Ph-III	40	60		

4.2 Upgradation/ Capacity Augmentation of 9 STPs (220 MLD)

Target – June, 2027

S No	Upgradation of existing STPs to achieve BOD:TSS 10/10			Status	Timelines
1	Yamuna Vihar Ph-I	10	15	The STPs is functional on existing parameters as BOD/TSS 30/50 mg/l. However, the tender for up-gradation and capacity augmentation shall be called after approval from the Apex Committee, since the Project is funded by GOI under AMRUT 2.0.	Dec-2026
2	Yamuna Vihar Ph-III	25	55	-do-	June-2027
3	Keshopur Ph-I	12	18	The STPs is functional on existing parameters as BOD/TSS 20/30 mg/l. However, the tender for up-gradation and capacity augmentation shall be called after approval from the Apex Committee, since the Project is funded by GOI under AMRUT 2.0.	Dec-2026
4	Okhla Ph-V	16	16	The STPs is functional on existing parameters as BOD/TSS 20/30 mg/l. However, the tender for up-gradation and capacity augmentation shall be called after approval from the Apex Committee, since the Project is funded by GOI under AMRUT 2.0.	Dec-2026
5	Mehruli	5	7.5		
6	Ghitorni	5	7.5		
7	Vasant Kunj Old	2.2	3.2		
8	Vasant Kunj New	3	4.5	The STPs is functional on existing parameters as BOD/TSS 30/50 mg/l. However, the tender for up-gradation and capacity augmentation shall be called after approval from the Apex Committee, since the Project is funded by GOI under AMRUT 2.0.	
9	Molar badh	0.66	0.66	The upgradation proposal is under estimation stage	Dec-2026

4.3 Creation of 40 DSTPs to meet the remaining 425 MLD capacity

Target – June, 2027

40 DSTPs are to be set-up in the Outer areas of North, North-West, West, South-West and South Delhi, covering over 400 U/A colonies and over 100 villages.

A. 13 DSTPs funded under AMRUT 2.0

Funds for these DSTPs have been funded by GoI under AMRUT 2.0 scheme. NITs for 13 DSTPs are being finalised in four packages and Tenders will be invited by the first week of May, 2025

B. Balance 27 DSTPs

The consolidated scheme for 27 DSTPs has been approved by EFC recently. The case is expected before the Cabinet for AA&ES very shortly and tenders are likely be invited by the end of May, 2025.

4.4 Creation of new STPs Delhi Gate, Shastri Park and Kailash Nagar (Approx. 100 MLD)

Target – March, 2028

During the inspection of DG NMCG on 24.04.2025, it was suggested to construct STP/DSTP on the mouth of the drain to trap it fully before discharge into river Yamuna.

4.5 Unauthorised Colonies (1799 nos.) to be sewerred

Target – March, 2028

Sl. No	Status	Status in Nos.
1	No. of Unauthorized Colonies where Sewer line laid	1226
2	No. of Unauthorized Colonies where sewer line work in progress	154
3	No. of Unauthorized Colonies where work is in Estimate /Tender / Award stage.	270
4	No. of Unauthorized Colonies where NOC is awaited from (Forest/ASI/ UD Deptt.)	99
5	No. of Unauthorized Colonies where sewer line will be laid 18 months after handing over possession of land for 2 DSTP	33
	Total	1782

4.6 Additional sewage treatment capacity of around 500 MLD

Target – March, 2029

Subject- Projection plan for additional 100MGD sewage treatment plants				
SN	Name of Plants	Present Capacity in MGD	Additional capacity required for future in MGD	Remark
1	Rohini STP	25	20	do
2	Rithala Ph- III STP	80	20	do
3	Pappankalan Ph-III STP	50	10	10MGD existing capacity argumentation is in progress and likely to be completed by June-25. Space is available for additional STP for future requirement or capacity argumentation of Pappankalan Ph-II from 20 to 30MGD or new STP
4	Nilothe Ph-III STP	60	15	20MGD existing capacity argumentation is in progress and likely to be completed by June-25. Space is available for additional STP for future requirement or capacity argumentation of Nilothe Ph-II from 20 to 30MGD or additional New STP
5	Keshopur Ph-IV STP	72	15	20MGD existing capacity argumentation is in progress and likely to be completed by March-25 & 6MGD by Dec-26. Space is available for additional STP at Keshopur STP premises.
6	Jagriti STP	0	20	Space available for future additional capacity requirement at Jagriti SPS premises.
7	Coronation new, Ph-VI STP	100	10	Space available for future requirement for construction of additional required capacity at Coronation STP
	Total		110	

6. Gap identification/Monitoring and Surveillance System

1. There are 22 drains which are outfalling into river Yamuna.
2. No further ISP is planned to trap sub drains.
3. As suggested by NMCG it is advisable to construct DSTP/STP at mouth of the drain for clean Yamuna.
4. Out of 22 drains, 2 major drain i.e. Najafgarh and Sahadra , possibility is being worked out to construct STP at mouth of the drain.
5. 11 Drains are already trapped.
6. Work for trapping of **2** drain at mouth is in progress.
7. STP/ DSTP is proposed to construct at mouth of 7 remaining drains.

6.2 Survey/ Assessment and DPR Preparation of each drain, Sewerage Zones for identification of gaps/left out drains/areas.

Target – June, 2027

S. No.	Summary - Availability of Sewerage Infrastructure			Nos. of Colonies
	TOTAL COLONIES LAID+BEING LAID			
1	STP- Commisioned	Sewer - Laid	HSC - Completed	846
2	STP- Commisioned	Sewer - Laid/Being Laid	HSC - Not Available	357
3	NOC Awaited	Sewer - Not Available	HSC - Not Available	99
4	STP- Not Available	Sewer - Laid/Being Laid	HSC - Not Available	177
5	STP- Not Available	Sewer - Not Available	HSC - Not Available	270
6	STP- Land Not Available	Sewer - Not Available	HSC - Not Available	33
Total				1782

6.4 Water Quality/flow measurements at Sahadara Drain Najafgarh Drain (Sahibi River)/Other Drains/Interstate Drains

Target – March, 2026

1. Flow measurement of the drain pertains to Drain Owning Agency.
2. Water quality of the drain is being monitored by DPCC/ CPCB.
3. NMCG suggested for independent monitoring of quality and quantity of all drains which are outfalling into river Yamuna directly.

9. Septage and Dairy Waste Management

9.1 FSTP REQUIREMENT/SERVICE PROVIDER MECHANISM (SEPTAGE COLLECTION) FOR UNSEWERED AREAS

TARGET – JULY, 2025



1. Unauthorized Colonies
2. JJ clusters
3. Effective implementation of “Delhi Water Board Septage Management Regulations 2018” DWBSMR 2018 and its amendment
4. notified on 13.03.2024

9.1 FSTP REQUIREMENT/SERVICE PROVIDER MECHANISM (SEPTAGE COLLECTION) FOR UNSEWERED AREAS **TARGET – JULY, 2025**

No of Vehicles Authorised by DJB : **154**

No. of Functional SPSs for collection
of septage from vendors : **86**

Cumulative Septage Treated by DJB
(As on 31.03.2025) : **239.43** Crore litres

Collection & treatment of Septage : **10.78 Lakh liters/Day**



9.1 DELHI WATER BOARD SEPTAGE MANAGEMENT REGULATION 2018

Delhi Water Board Septage Management Regulation 2018” were notified by the U D Department, GNCTD on **12.11.2018** and necessary action is to be taken by DJB, DMs and LBs / MCD.

U D Dept., GNCTD notified an amendment in “Delhi Water Board Septage Management (Amendment) Regulation on 13.03.2024 including following in the existing Regulations:

1. (a) Penalty for deposit of septage by unauthorized (unlicensed) entities shall be Rs. 50,000/- plus confiscation of vehicle.
(b) Penalty for disposal of Septage at places other than the designated places by authorized licensee shall be Rs. 50,000/- per violation.
(c) Penalty on a person who uses the services of unlicensed vendors/vehicles for discharging the septage shall be Rs. 10,000/- per violation.
1. An officer not lower than the rank of Naib Tehsildar in DM offices, JE in DJB /I&FC, Sub Inspector in Delhi Police and Sanitary Inspector in CD shall be competent to impose penalty

Installation of GPS System - Each Vehicle used for transportation of septage shall be fitted with GPS device and access rights of the movement data shall be given to the Delhi Jal Board for tracking of such vehicles

9.3 Creation of Fecal Sludge Treatment Plants (in Peri-Urban Areas)

Target – June, 2027

1. Possibility is being worked out FSTP for septage collection for unsewered area.
2. NMCG has principally agreed for funding for FSTPs.

Improvement in E flows at Delhi downstream

- The additional flow (equivalent 5.69 cumecs) in River Yamuna imparted through the outfall of Okhla STP of capacity 564 MLD, will be taken out downstream of Okhla barrage through Yamuna Canal. Thus, Okhla treated wastewater of 5.69-cumecs will partially provide relief to River Yamuna **Target – Feb, 2026**

- The work of laying of 2800 mm dia MS Line pipe through Microtunneling for discharging high quality treated effluent (BOD<10, TSS<10) from Okhla STP to downstream of Okhla Barrage via Abul Fazal Drain, was awarded by DJB vide work order No.02 (2022-23) dated 12.08.2022.
- The scope of work included total length of 225 m of 2800 mm dia pipe out of which 93m along the Jasola Road has been laid.
- Further work of connecting the line to Abul Fazal Drain was held up due to permission from UP Irrigation. The permission from UP Irrigation was received on 01.03.2025.
- Presently, the balance work is in progress and is likely to be completed by Sep-2025.

Thank You

